


- Stage 3 - Seismic Bracing and associated work (generally includes but not limited to)**
- Seismic bracing abatement including all NON structural materials located directly within the limits of construction
 - Seismic bracing abatement including all NON structural materials located indirectly within the limits of construction (areas associated with this work)
 - Bracing limits of construction de-commissioning
 - Removal and storage of fixed existing equipment and fixed furnishings
 - Bracing preparation
 - Construction pathway preparations
 - Bracing installation
 - Bracing limits of construction re-construction
 - Reinstallation of fixed existing equipment and fixed furnishings
 - Bracing limits of construction re-commissioning
 - Bracing pathway repairs and re-commissioning
 - MEP completion of work
 - MEP commissioning
 - Fireproofing of abated /exposed structure
 - Bracing Sequence
 - Zone 1 (C1,C2,C3)
 - Zone 2 (A1,D1,D2)
 - Zone 3 (A3,B1,B2)
 - Zone 4 (D3,D4,D5)
 - Zone 5 (A2,A4)

Stage 3 - Seismic Bracing and associated work (generally includes but not limited to):
 A. Start Date – Stage 1 Completion
 B. Duration – 21 Months (completion date +28.5 months from NTP)

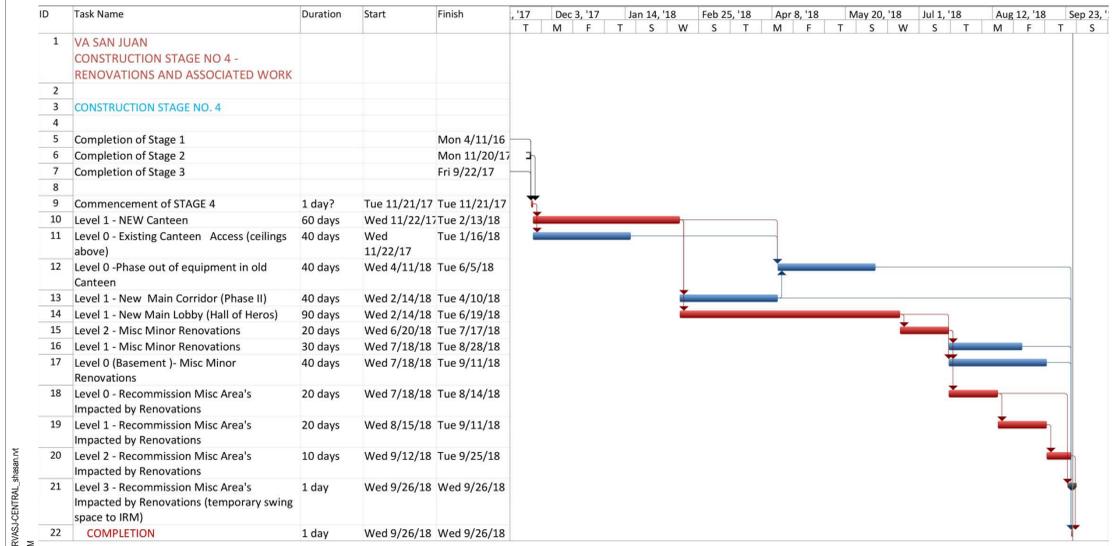

- Stage 4 - Renovation and associated work (generally includes but not limited to)**
- Abatement at all renovated area including all NON structural materials located directly within the limits of construction
 - Abatement of all renovated areas including all NON structural materials located indirectly within the limits of construction (areas associated with this work)
 - Temporary protection of existing hospital facilities
 - Renovation limits of construction de-commissioning
 - Removal and storage of fixed existing equipment and fixed furnishings
 - Renovation preparation
 - Renovation construction pathway preparations
 - Renovation
 - Renovation limits of construction re-construction
 - Reinstallation of fixed existing equipment and fixed furnishings
 - Renovation pathway repairs and re-commissioning
 - Interior Demolition of all abated areas (future shelled space)
 - MEP completion of work
 - MEP commissioning
 - Fireproofing of abated /exposed structure
 - Renovation Sequence
 - Level Basement
 - Level 3
 - Level 1 (see stage 2 for urology and associated areas)
 - Level 2
 - Demobilization
 - Contractor to restore all interruption of site and landscape to existing condition prior to beginning of project, and bring all areas within the construction fence to clean and stable condition.
 - Contractor to remove construction and all construction material and equipment.
 - Contractor to turn over site to VAHS.

Stage 4 - Renovation and associated work (generally includes but not limited to):
 A. Start Date – Stage 3 Completion
 B. Duration – 10 months (completion date = 38.5 months from NTP)

NO	REVISIONS	DATE
1	ADDENDUM # 1	07/07/2015
	BID SET	06/12/2015

CONSULTANTS:
GAUTIER de TORRES ARQUITECTOS
 Apartado 19357, San Juan, Puerto Rico 00910-1357
DEGENKOLB ENGINEERS
 235 MONTGOMERY ST SUITE 500, SAN FRANCISCO, CA 94104
SAQ ENVIROMENTAL ENGINEERS, INC
 PO.BOX 155, MANATI, PR 00674

LASALLE ENGINEERING, LLC
 1000 YORK ROAD WILLOW GROVE, PA 19090
M.A + ASSOCIATES, LLC
 8655 CHERRY LANE, LAUREL, MD 20707
CT + ASSOCIATES, LLC
 86 THOMAS LEIGHTON BLVD, CUMBERLAND, RHODE ISLAND 02864

ARCHITECTS/ENGINEERS
HR
 1101 King Street Suite 400,
 Alexandria, VA 22314

Drawing Title CONSTRUCTION STAGING SEQUENCE	Project Number 672-085A
Approved : Project Director	Building Number 1
Date 06/12/2015	Checked by TA
	Drawn SH

Project Title PHASE 3 BUILDING ONE-SEISMIC CORRECTIONS AND RENOVATIONS	Drawing number GP-101
Location VA Caribbean Healthcare System 10 Casia Street, San Juan, PR 00921-3201	
Date 06/12/2015	Checked by TA
	Drawn SH

**BUILDING PARTIALLY SPRINKLERED (RENOVATED SPACES/
 NEW PENTHOUSES IN THIS SCOPE OF WORK 100% SPRINKLERED)
 BID SET 06/12/2015**

Office of
 Construction
 and Facilities
 Management
 Department of
 Veterans Affairs
