

VA



U.S. Department of Veterans Affairs

Office of Information and Technology

IT Operations and Services

| Solution Delivery

COMMUNITY BASED OUTPATIENT CLINIC (CBOC) INSIDE PLANT INFORMATION TRANSPORT SYSTEMS SPECIFICATIONS

DEVELOPED BY:
DATA CENTER ENGINEERING
DATA CENTER & CLOUD ENGINEERING

Department of Veterans Affairs



*IT Operations and Services
Solution Delivery*



PROJECT:

*CBOC ITS
SPECIFICATIONS*

PROJECT No:

N/A

MARK	DATE	DESCRIPTION

ISSUE:

DRAWING No:

FILE: CBOC INSIDE PLANT ITS SPEC V1.vsd

DRAWN BY: Kevin Grzelka

CHECKED BY: Michael Julian, RCDD

DOC VERSION No: 1.0

PRINT DATE: Oct 5, 2017

ISSUE DATE: Oct 5, 2017

SHEET TITLE

COVER PAGE

COVER

SHEET: 1 OF 15

FRONT MATTER

PURPOSE:

THIS DRAWING SET REPRESENTS THE COMPUTING AND PASSIVE INFRASTRUCTURE DESIGN AND RACK ELEVATIONS FOR A GENERIC HEALTHCARE FACILITY EQUIPMENT ROOM (ER) AND A GENERIC TELECOMMUNICATION ROOM (TR). UNLESS NOTED OTHERWISE, ACTIVE EQUIPMENT WILL BE FURNISHED AND INSTALLED BY VA OR VA CONTRACTORS. THE STRUCTURED CABLING PLANT INSTALLERS WILL FURNISH AND INSTALL PASSIVE CABLE PLANT INFRASTRUCTURE INCLUDING HORIZONTAL CABLE MANAGERS, UTP AND FO HORIZONTAL CABLE, PATCH PANELS, PATHWAY RACKS, FIBER DISTRIBUTION CABINETS AND FIBER CASSETTES.

DESIGN OBJECTIVES

1. MODULARITY:
- THIS DESIGN IS HIGHLY MODULAR.
2. FLEXIBLE:
- THIS DESIGN IS FLEXIBLE TO ACCOMMODATE CHANGES TO FLOOR PLANS.
3. CABLE PLANT:
- UTP CATEGORY 6A CABLE PLANT WILL SUPPORT 10 GIGABIT ETHERNET.
- FIBER PLANT WILL UTILIZE LASER ENHANCED OM4 40 GbE RATED 50/125 MULTIMODE.

THIS DRAWING IS SCALED TO 11X17 FORMAT.

DRAWING TYPE DEFINITIONS

- T0 - Campus or Site Plans - Exterior Pathways and Inter-Building Backbones
- T1 - Layout of complete building per floor - Serving Zone Boundaries, Backbone Systems, and Horizontal Pathways
- T2 - Serving Zones Drawings - Drop Locations and Cable ID's
- T3 - Communication Equipment Rooms - Plan Views - Tech and AMEP /Elevations - Racks and Walls Elevations
- T4 - Typical Detail Drawings - Faceplate Labeling, Firestopping, ADA, Safety, DOT, etc...
- T5 - Schedules (Cabling and Equipment Spreadsheets) for cutovers

Standard or Document Description

- ANSI/TIA-606-C, Administration Standard for Telecommunications Infrastructure
- ANSI/TIA-606-B-1, Administration Standard for Telecommunications Infrastructure Addendum 1- Automated Infrastructure Management Systems - Addendum to ANSI/TIA-606-B
- ANSI/TIA-607-C, Generic Telecommunications Bonding and Grounding (Earthing) for Customer Premises
- ANSI/TIA-607-C-1, Generic Telecommunications Bonding and Grounding (Earthing) for Customer Premises - Addendum to TIA-607-C
- ANSI/TIA-942-A, Telecommunications Infrastructure Standard for Data Centers
- ANSI/TIA-942-A-1, Telecommunications Infrastructure Standard for Data Centers Addendum 1- Cabling Guidelines for Data Center Fabrics - Addendum to TIA-942-A
- ANSI/TIA-1179, Healthcare Facility Telecommunications Infrastructure
- BICSI 002, Data Center Design and Implementation Best Practices
- BICSI ITSIMM, Information Technology Systems Installation Methods Manual (ITSIMM) - 7th Edition
- BICSI/NECA 568, Standard for Installing Commercial Building Telecommunications Cabling
- BICSI/NECA 607 Standard for Telecommunications Bonding and Grounding Planning and Installation Methods for Commercial Buildings 2011
- CSI MASTERFORMAT™ 2004 EDITION NUMBERS & TITLES Construction Specifications Institute (CSI)
- NFPA 70, National Electrical Code
- NFPA 75, Standard for the Fire Protection of Information Technology Equipment



PROJECT:

CBOC ITS
SPECIFICATIONS

PROJECT No:

N/A

MARK	DATE	DESCRIPTION
------	------	-------------

ISSUE:

DRAWING No:

FILE: CBOC INSIDE PLANT ITS SPEC V1.1.vsd

DRAWN BY: Kevin Grzelka

CHECKED BY: Michael Julian, RCDD

DOC VERSION No: 1.0

PRINT DATE: Oct 5, 2017

ISSUE DATE: Oct 5, 2017

SHEET TITLE

FRONT MATTER

FRONT MATTER

SHEET: 2 OF 15

T2 SYMBOLS

- DATA
- W WALL PHONE
- FLOOR MOUNT
- F FIRE ALARM PANEL
- E EMERGENCY PHONE
- D SECURITY OR FIRE ALARM DIALERS
- DATA / TELEPHONE
- TELEPHONE
- CR SECURITY SYSTEM CARD READER
- CC CLOSED CIRCUIT SURVEILLANCE CAMERA OUTLET
- MD MOTION DETECTOR

T3 SYMBOLS

- TWIST LOCK RECEPTACLE
- T THERMOSTAT
- QUADRUPLEX OUTLET
- 110 RECEPTACLE
- TGB TELECOMMUNICATIONS GROUNDING BUSBAR
- STRIP LIGHT
- SERVICE PANEL
- HORIZONTAL SLEEVE (SIZE AS INDICATED)
- CONDUIT (SIZE AS INDICATED)
- VERTICAL SLEEVE (SIZE AS INDICATED)
- CABLE RACEWAY
- TELECOMMUNICATIONS OUTLET

T4 SYMBOLS

- CHATSWORTH SERVER RACK. 24"WIDE X 47.5" DEEP
- PERFORATED FLOOR TILE
- OR-60401015
- OR-M2LCQ24-50E
- OR-MM6HM61RU
- FC01U-P
- zPDU (R/F)
- L21-30
- L21-20
- IEC 320-C19
- IEC 320-C20
- IEC 320-C13
- IEC 320-C14
- OR-MM20730-W. 30" DEEP CHANNEL 7'H. 45RU. ORTRONICS MM20 CHANNEL RACK



PROJECT:
CBOC ITS SPECIFICATIONS

PROJECT No:
N/A

MARK	DATE	DESCRIPTION

ISSUE:

DRAWING No:

FILE: CBOC INSIDE PLANT ITS SPEC V1.1.vsd

DRAWN BY: Kevin Grzelka

CHECKED BY: Michael Julian, RCDD

DOC VERSION No: 1.0

PRINT DATE: Oct 5, 2017

ISSUE DATE: Oct 5, 2017

SHEET TITLE

SYMBOLS


SYMBOLS

SHEET: 3 OF 15


N/A

<i>MARK</i>	<i>DATE</i>	<i>DESCRIPTION</i>

SHEET: 4 OF 15

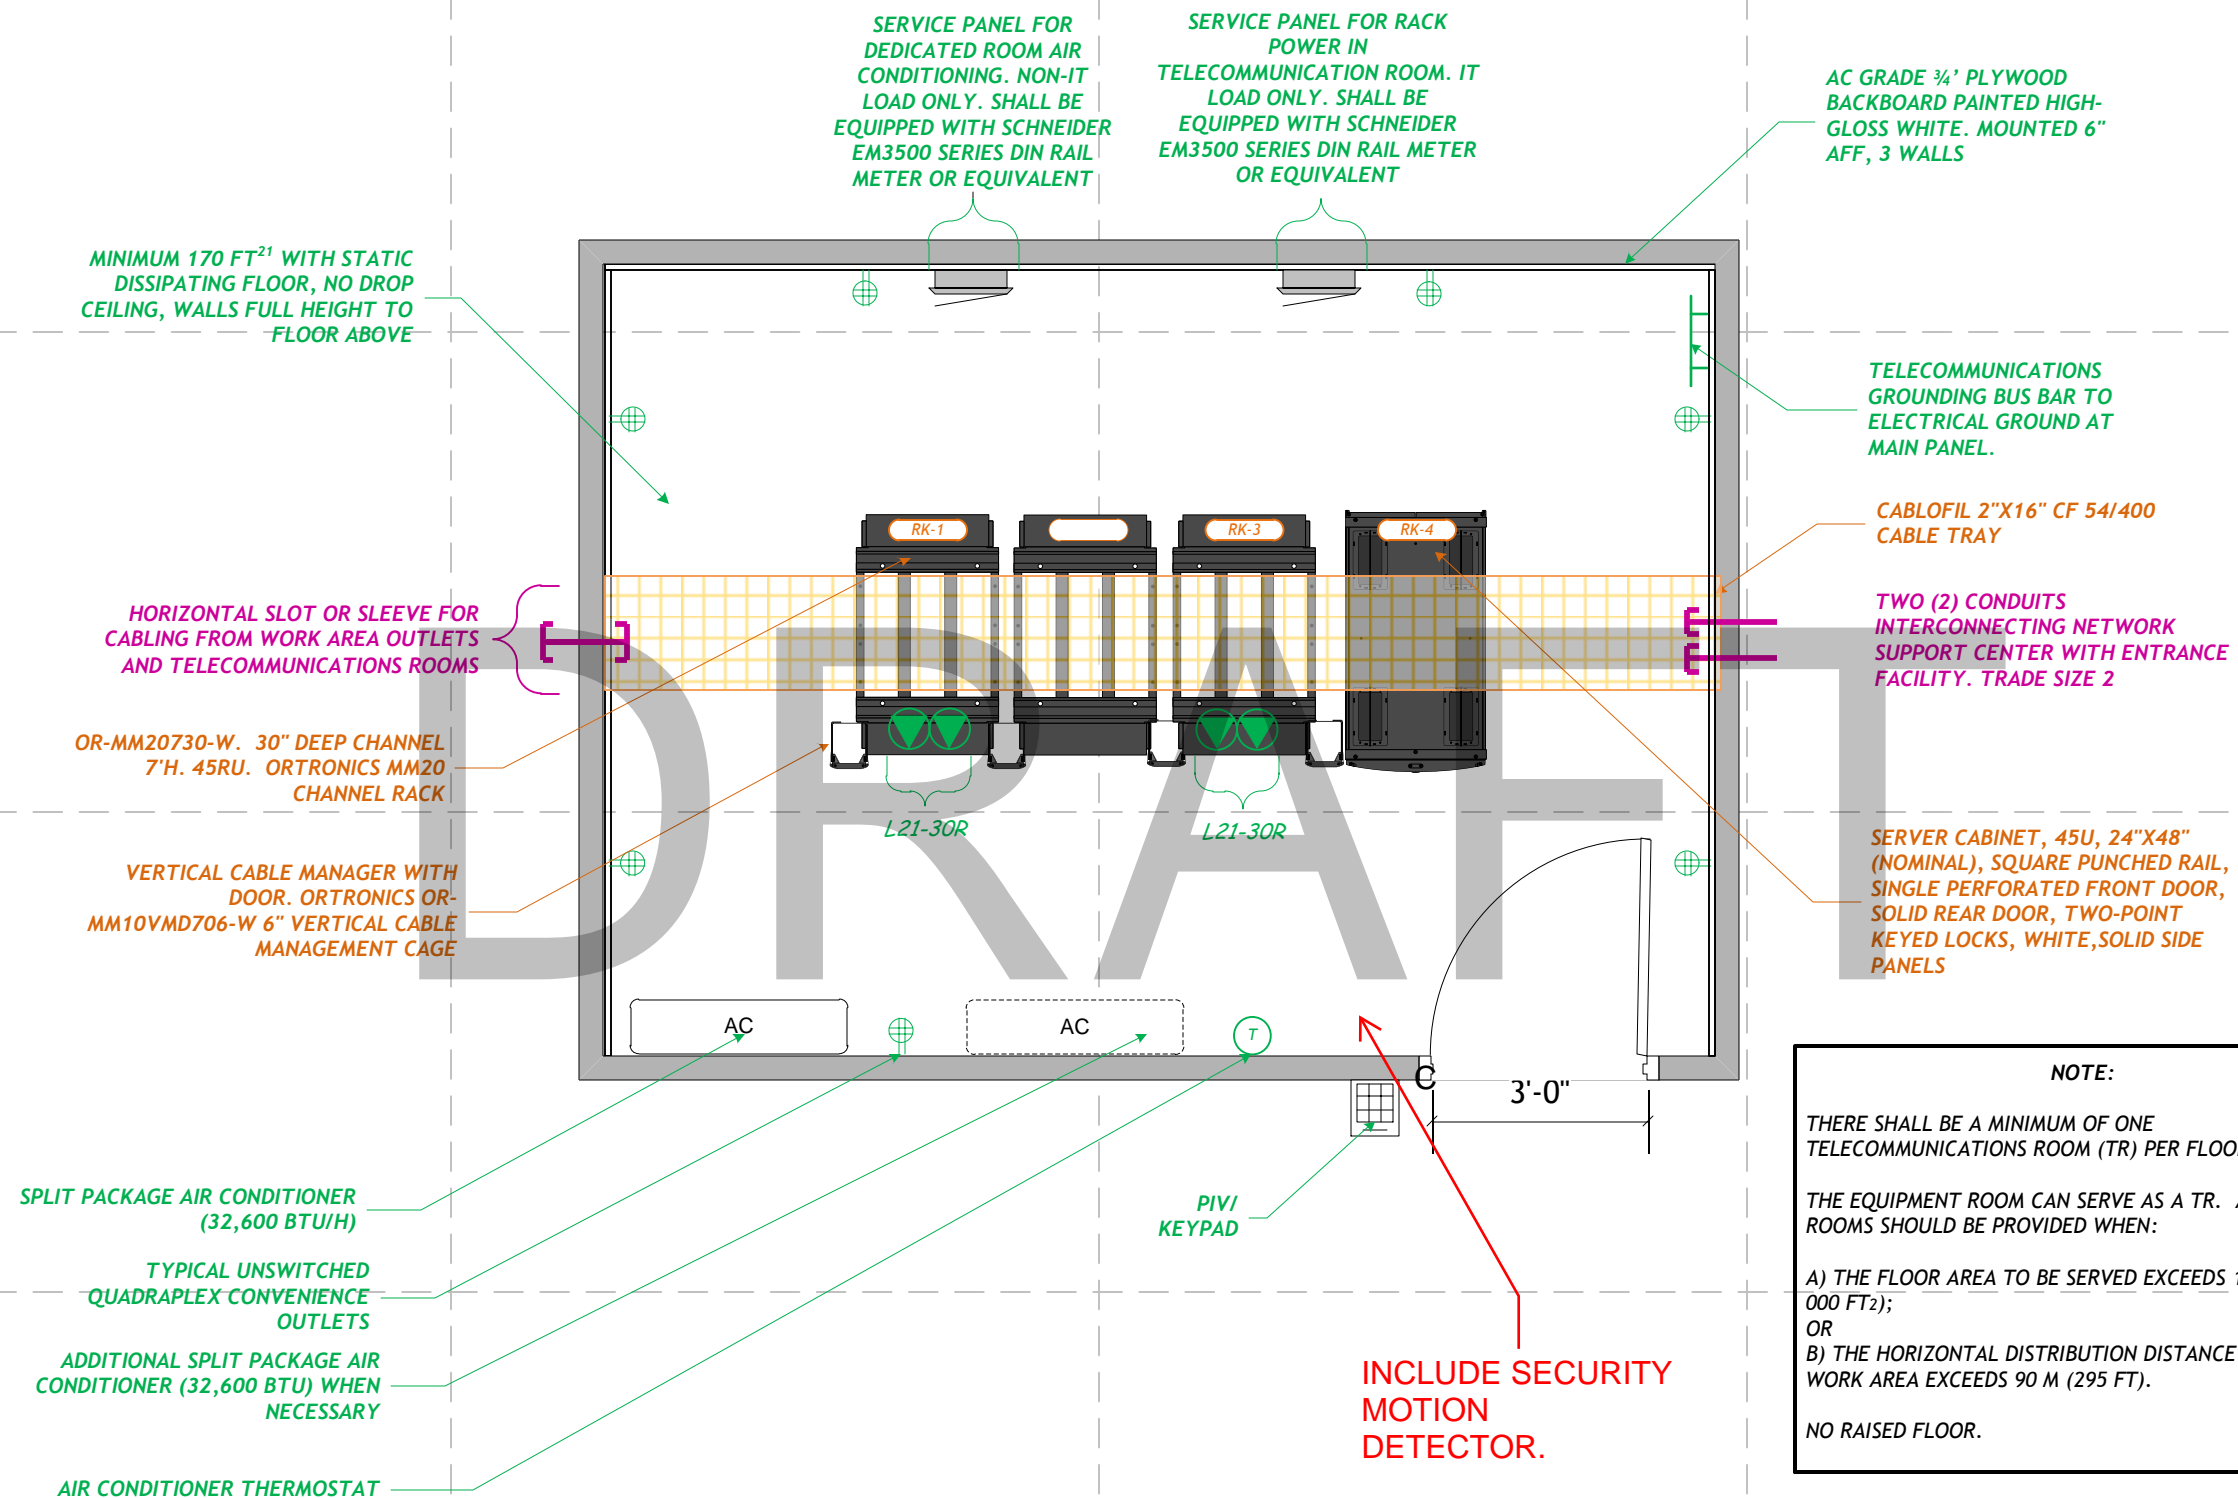

GENERIC FLOOR PLAN FOR HEALTH CARE FACILITY EQUIPMENT ROOM

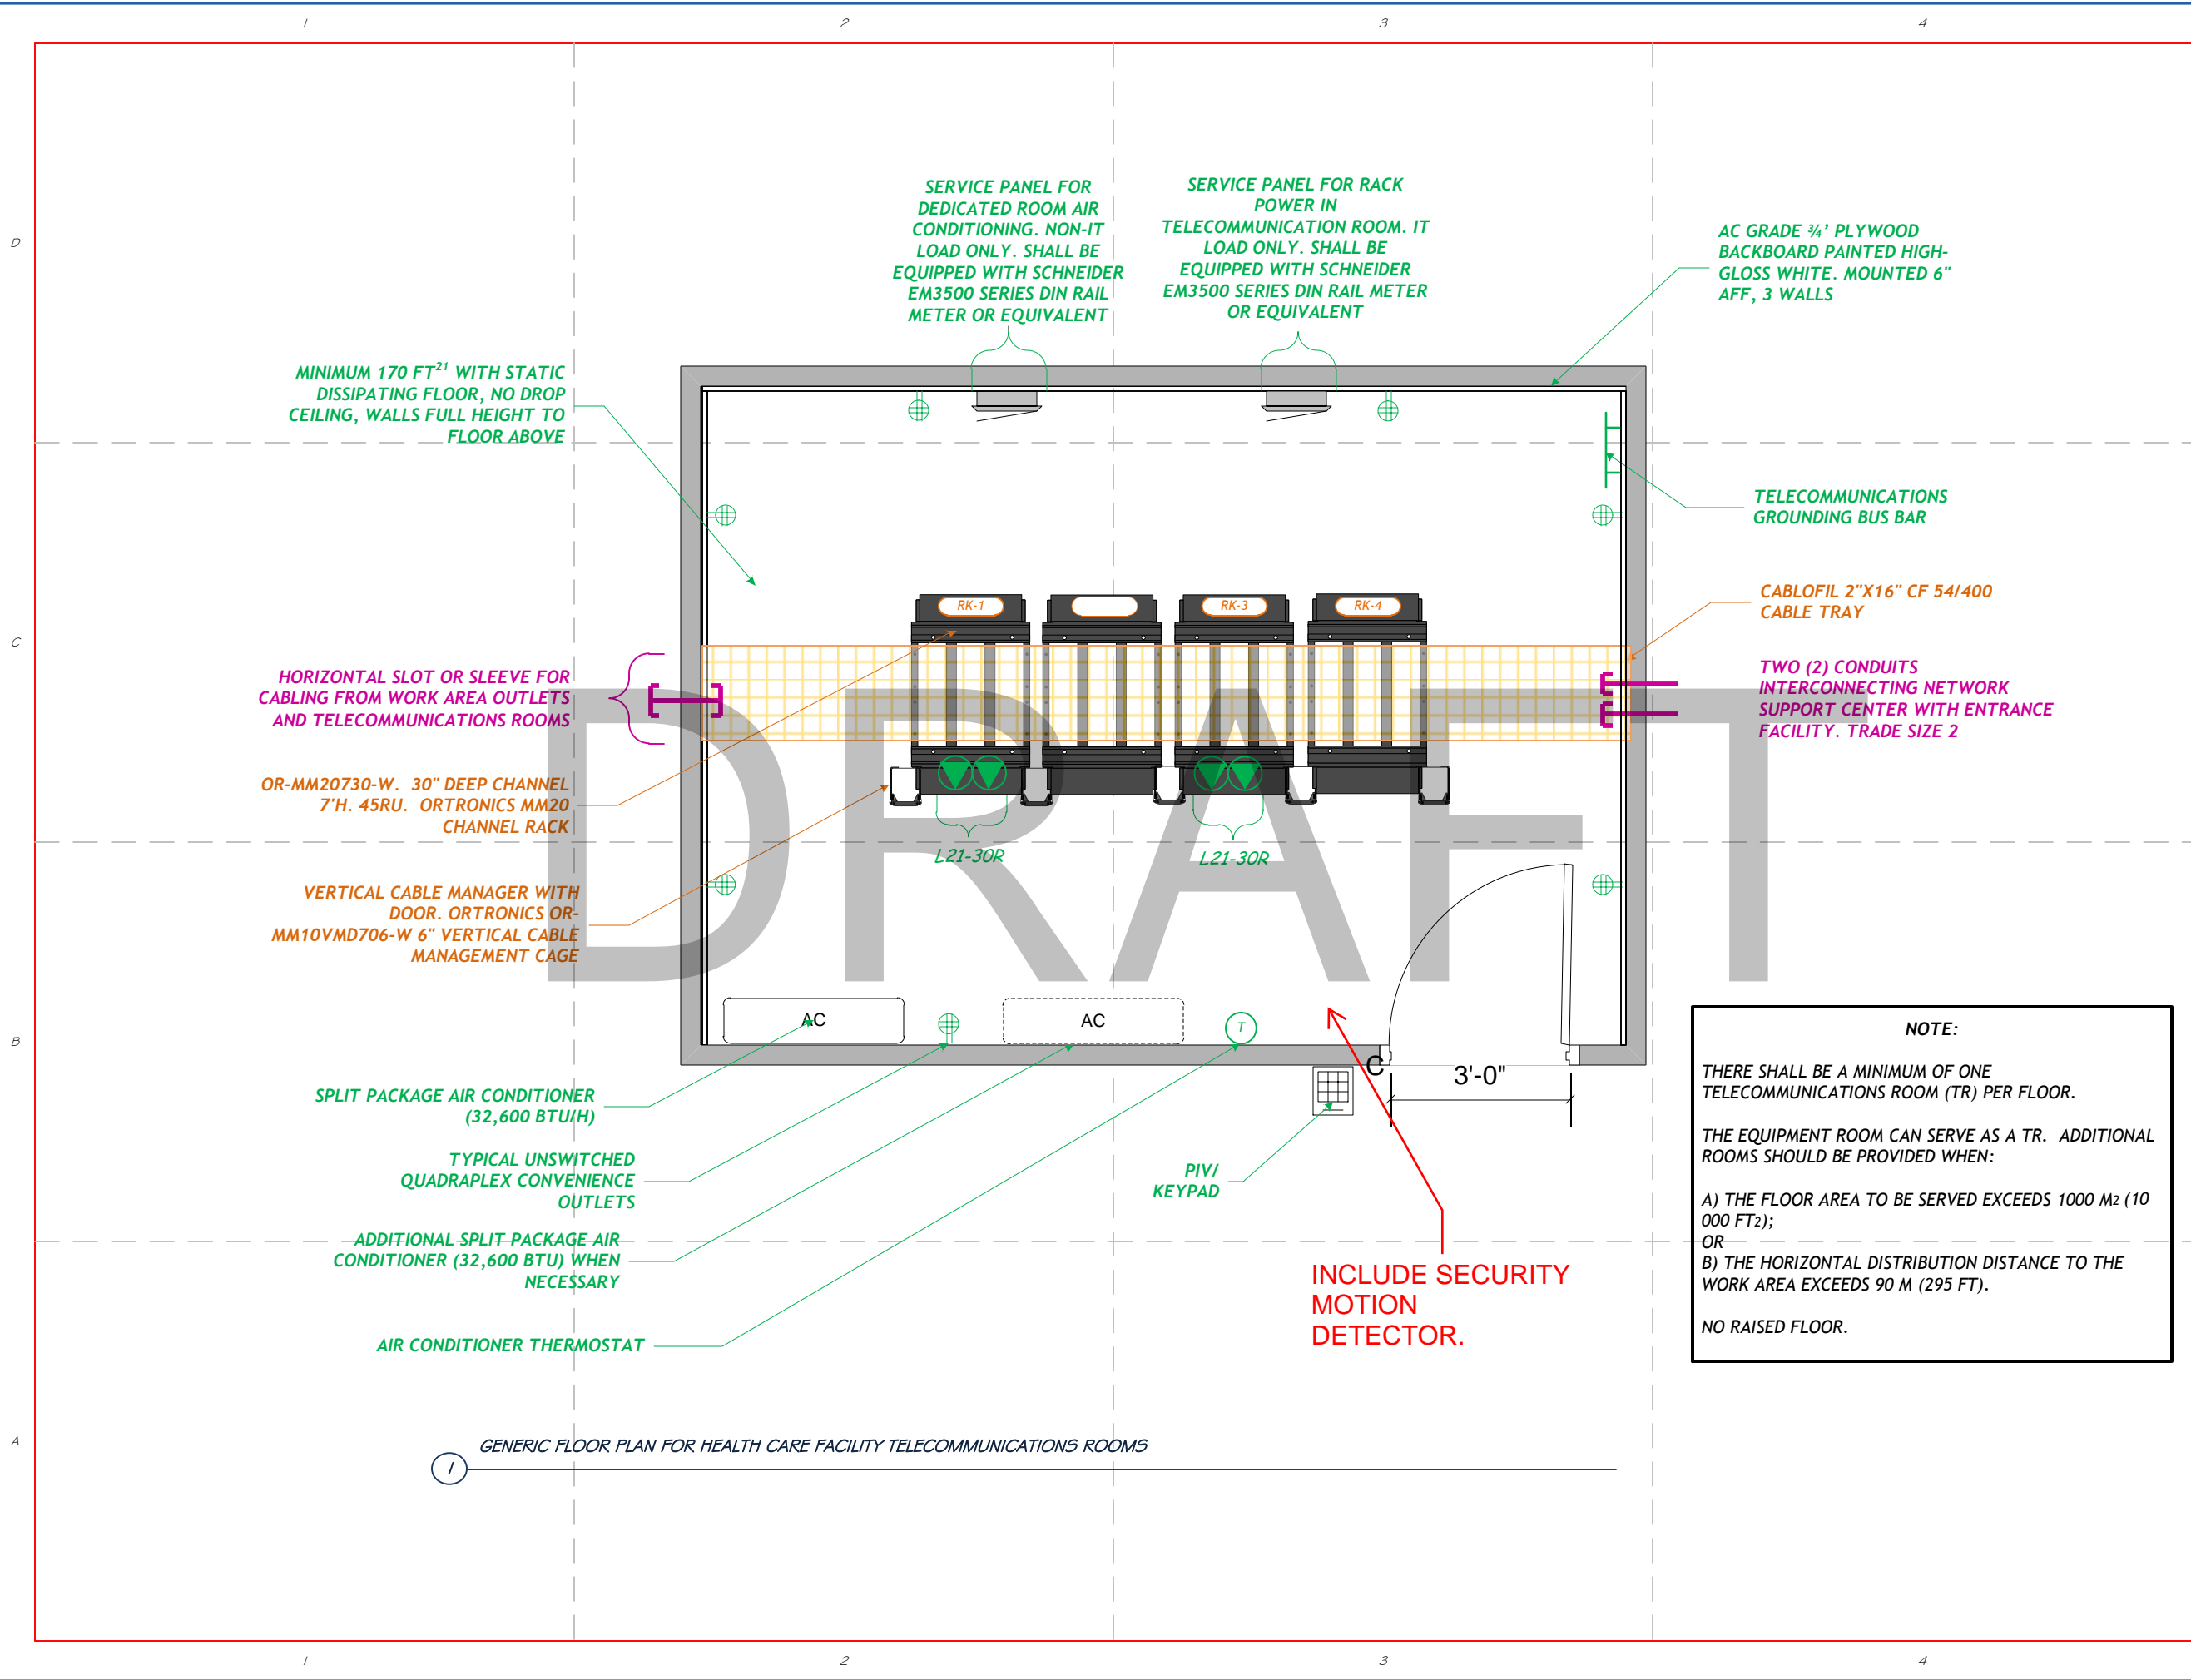

PROJECT:

CBOC ITS
SPECIFICATIONS

PROJECT No:

N/A

MARK	DATE	DESCRIPTION
------	------	-------------

ISSUE:

DRAWING No:

FILE: CBOC INSIDE PLANT ITS SPEC V1.1.vsd

DRAWN BY: Kevin Grzelka

CHECKED BY: Michael Julian, RCDD

DOC VERSION No: 1.0

PRINT DATE: Oct 5, 2017


ISSUE DATE: Oct 5, 2017

SHEET TITLE

TELECOMMUNICATIONS
ROOM

T3-GENERIC HEALTH CARE
FACILITY TR

SHEET: 5 OF 15

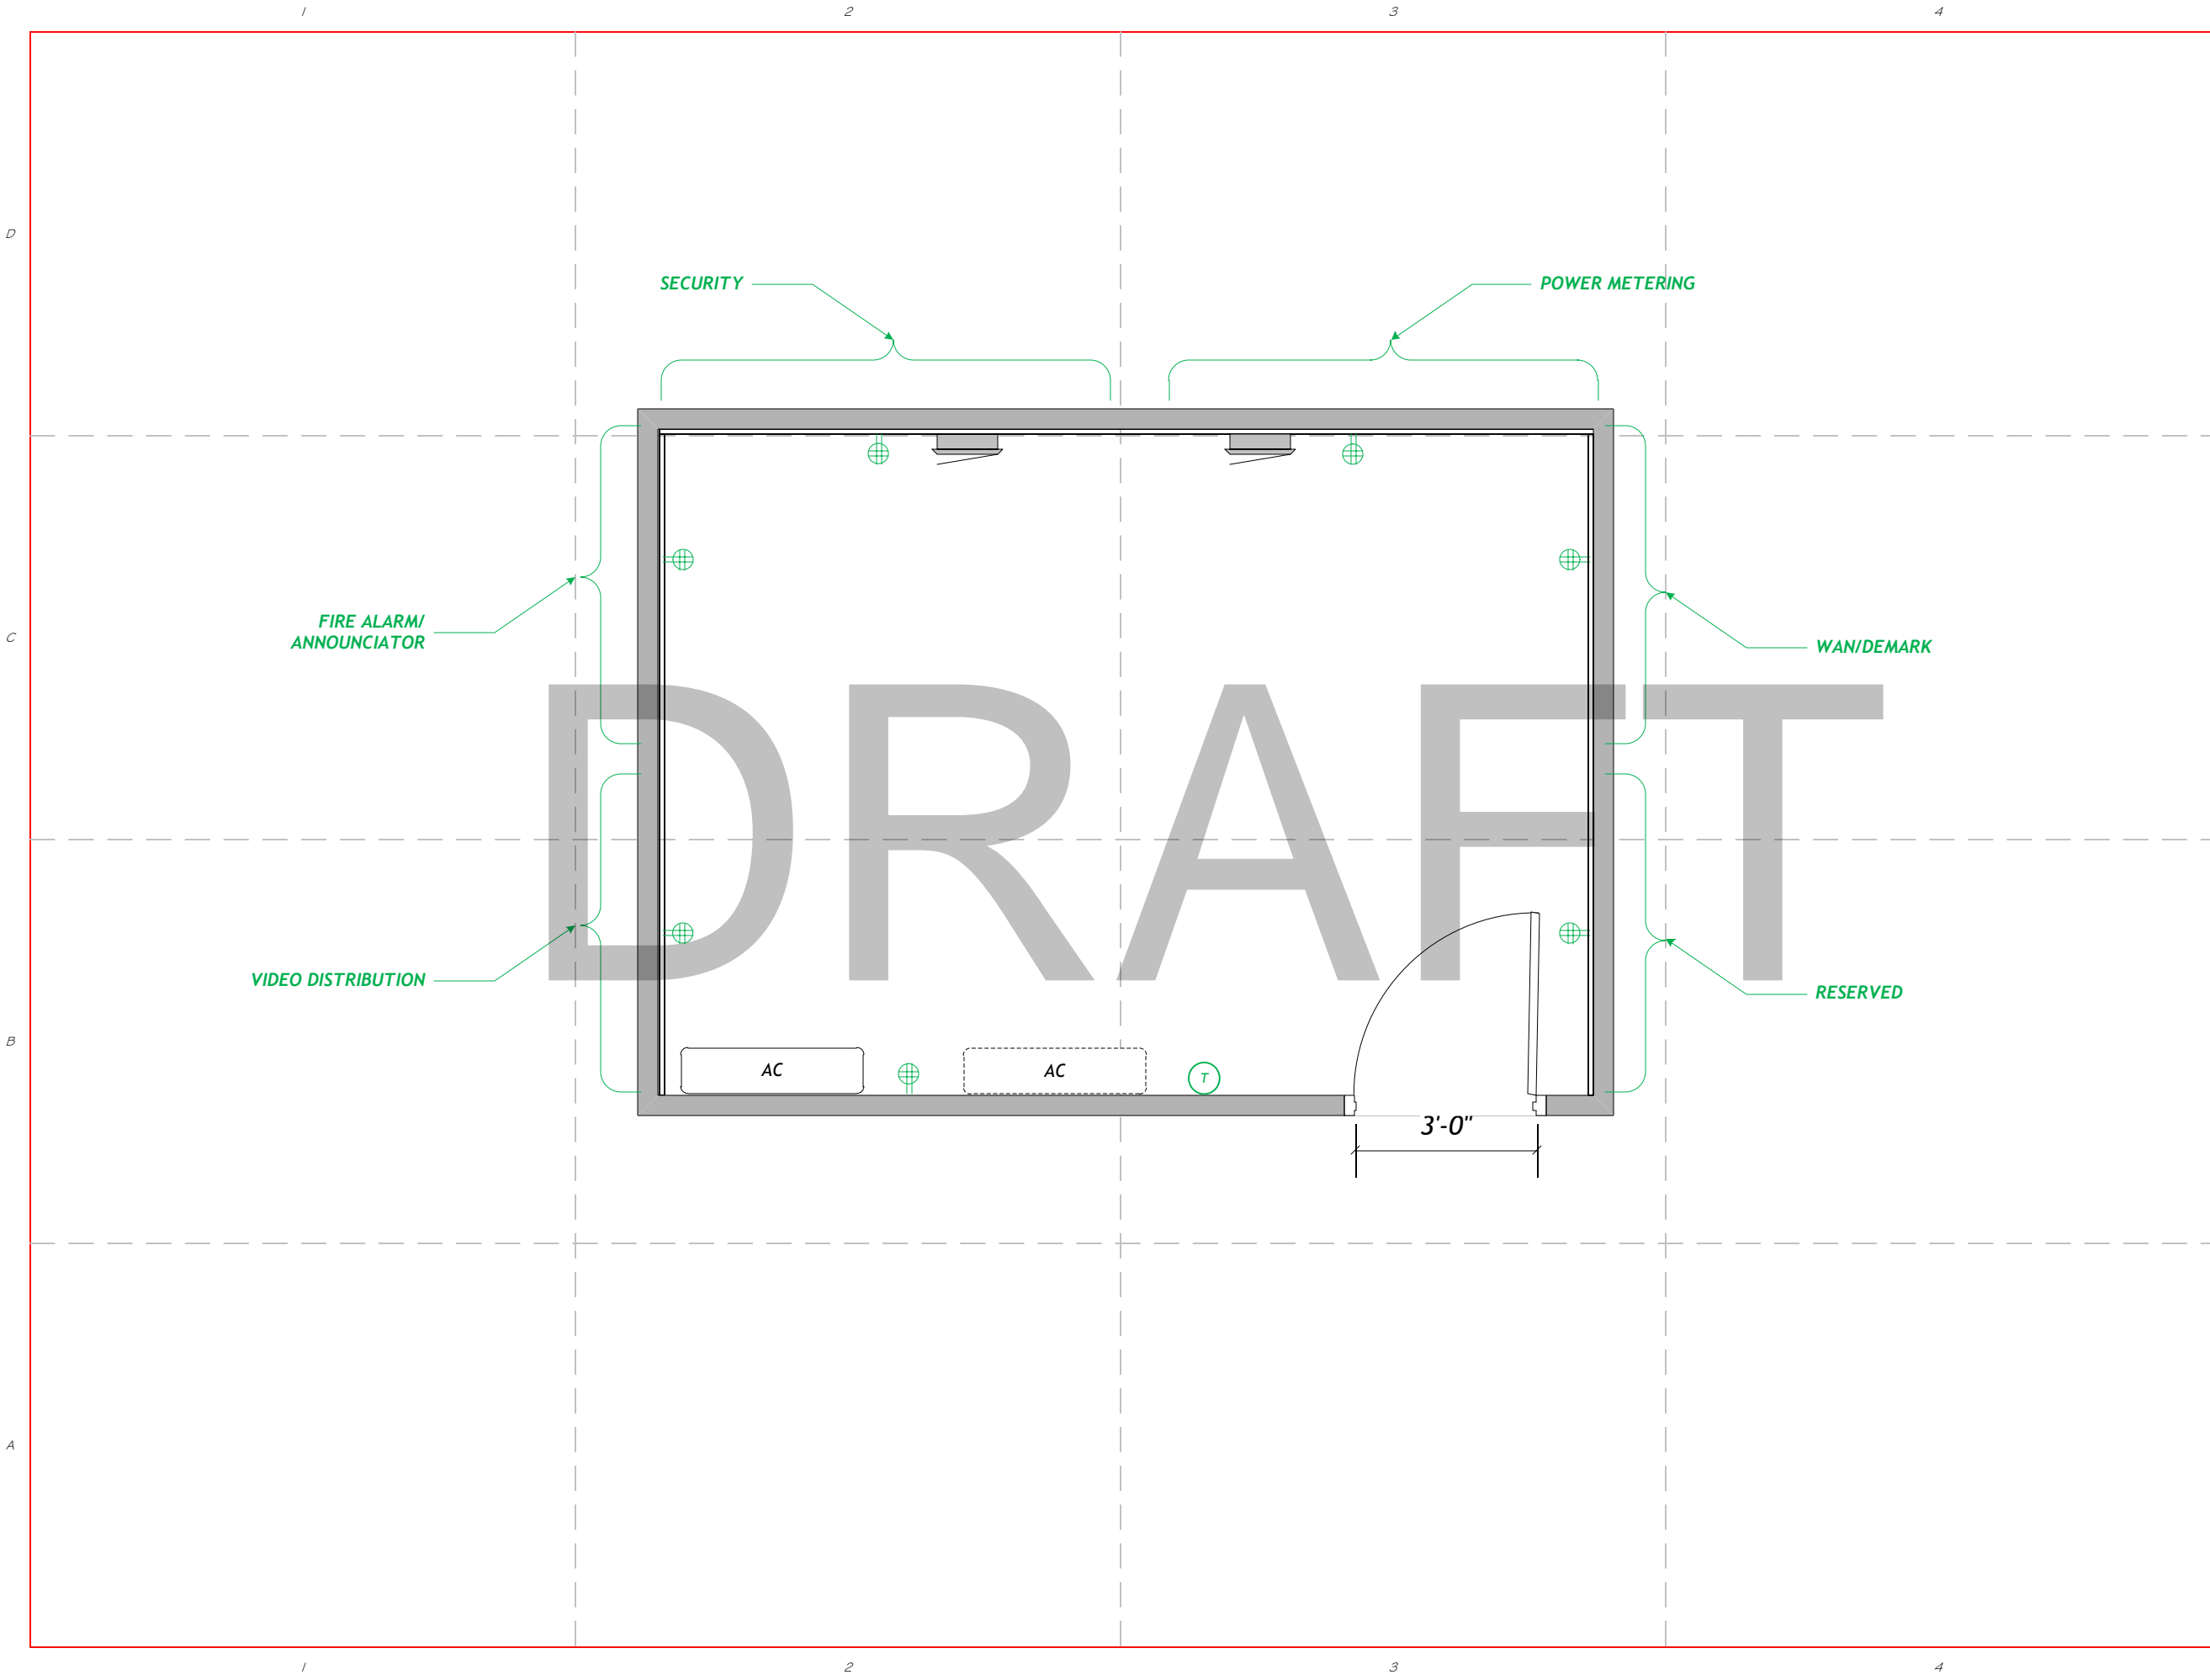

PROJECT:
CBOC ITS
SPECIFICATIONS

PROJECT No:
N/A

MARK	DATE	DESCRIPTION


ISSUE:	
DRAWING No:	
FILE:	CBOC INSIDE PLANT ITS SPEC V1.vsd
DRAWN BY:	Kevin Grzelka
CHECKED BY:	Michael Julian, RCDD
DOC VERSION No:	1.0
PRINT DATE:	Oct 5, 2017
ISSUE DATE:	Oct 5, 2017
SHEET TITLE	

TYPICAL BACKBOARD
ELEVATION


VA

<i>MARK</i>	<i>DATE</i>	<i>DESCRIPTION</i>

SHEET: 7 OF 15

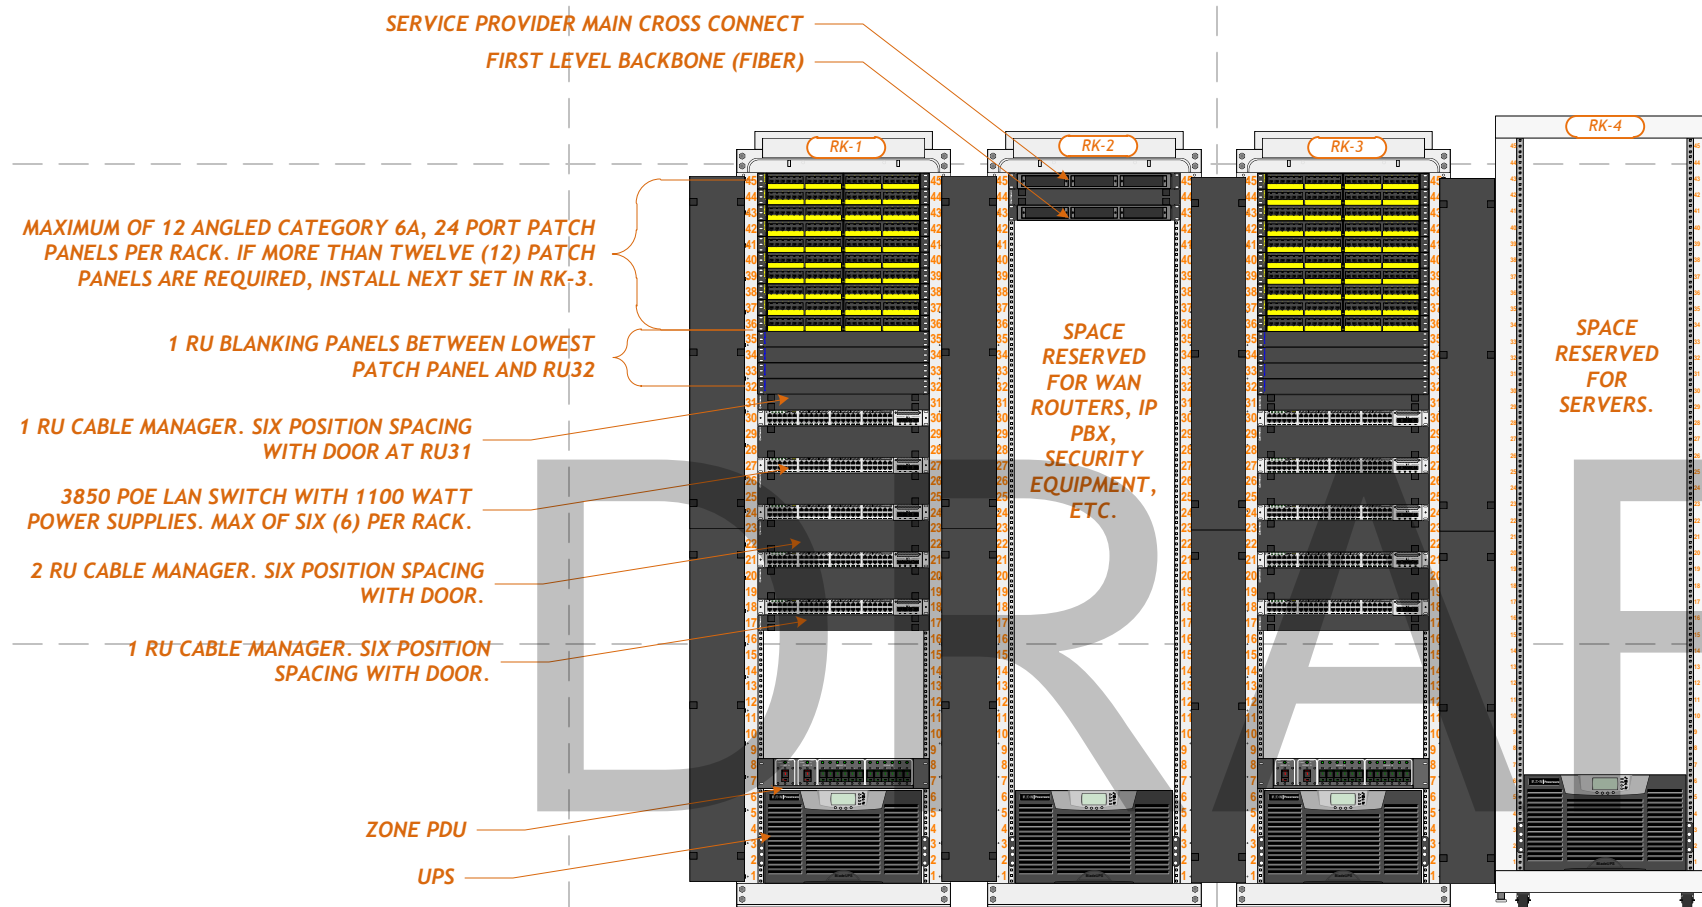

TYPICAL RACK ELEVATION FOR HEALTH CARE FACILITY TELECOMMUNICATIONS ROOMS



KIT INCLUDES:
(1) TOP DOOR SUPPORT
(1) LOWER DOOR SUPPORT
WITH 2 FAN OPENINGS

OR-MM20724PDHD-W	WHITE
OR-MM20724PDHD-B	BLACK
PART NO	COLOR

PART NUMBER DESIGNATIONS



NTS



NTS



NTS

TYPICAL ENCLOSURE SPECIFICATION

NTS



N/A

<i>MARK</i>	<i>DATE</i>	<i>DESCRIPTION</i>

SHEET: 9 OF 15



PROJECT:

CBOC ITS
SPECIFICATIONS

PROJECT No:

N/A

MARK	DATE	DESCRIPTION
------	------	-------------

ISSUE:

DRAWING No:

FILE: CBOC INSIDE PLANT ITS SPEC V1.vsd

DRAWN BY: Kevin Grzelka

CHECKED BY: Michael Julian, RCDD

DOC VERSION No: 1.0

PRINT DATE: Oct 5, 2017

ISSUE DATE: Oct 5, 2017

SHEET TITLE


T4 - TYPICAL WORK AREA
OUTLETS

SHEET: 10 OF 15


NOTES:

TYPICAL WORK AREA OUTLET FACEPLATE WILL BE INSTALLED WITH CATEGORY 6A COMPONENT-COMPLIANT 8P8C MEDIA INTERFACE CONNECTORS (RJ45). EACH CONNECTOR WILL BE TERMINATED TO HIGH QUALITY CATEGORY 6A HORIZONTAL CABLING WHICH WILL TERMINATE IN THE TELECOMMUNICATIONS ROOM AS SPECIFIED ELSEWHERE IN THIS DESIGN PACKAGE. ALL HORIZONTAL UTP SHALL BE CATEGORY 6A AND TERMINATED TO T568B.


TYPICAL FACEPLATE WILL BE INSTALLED WITH TWO (2) RJ45s. HIGH DENSITY FACEPLATES WILL BE ISNTALLED WITH FOUR (4) RJ45s.




ALL LABELING SHALL BE ANSI/TIA/EIA/606C COMPLIANT. BLACK LETTERING ON WHITE FIELD. MACHINE PRINTED. FURTHER GUIDANCE ON ADMINISTRATION MAY BE SPECIFIED IN OTHER SECTIONS OF THIS DESIGN PACKAGE.

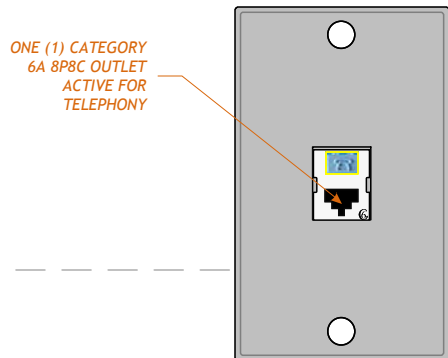


3 TYPICAL WALL MOUNT PHONE OUTLET
NTS

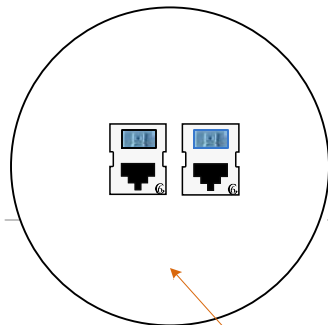


1 TYPICAL WORK FLOOR MOUNT OUTLET
NTS

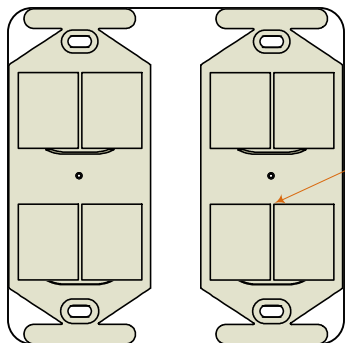

DUAL GANG WORKBOX
WITH TWO CONNECTOR
CHASSIS.

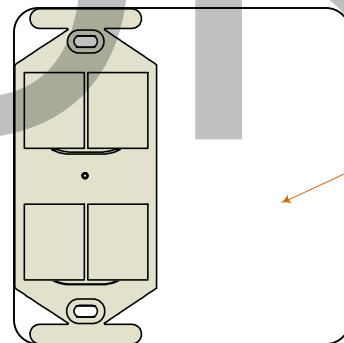


DUAL GANG WORKBOX
WITH ONE CONNECTOR
CHASSIS.

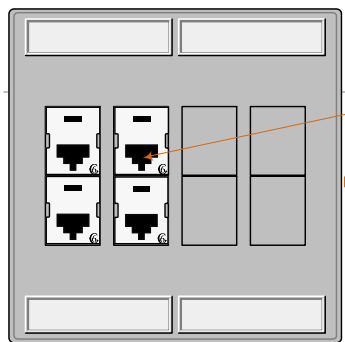

FOUR (4) CATEGORY 6A
8P8C OUTLETS ACTIVE
FOR TELEPHONY/DATA

EIGHT (8) POSITION
FACEPLATE MOUNTED ON
DUAL GANG WORKBOX.
FACEPLATE COLOR
SPECIFIED BY OTHERS.



4 TYPICAL HIGH DENSITY WALL MOUNTED WORK AREA OUTLET
CONFIGURATION

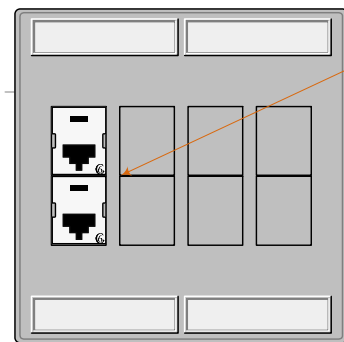


TWO (2) CATEGORY 6A
8P8C OUTLETS ACTIVE
FOR TELEPHONY/DATA

EIGHT (8) POSITION
FACEPLATE MOUNTED ON
DUAL GANG WORKBOX.
FACEPLATE COLOR
SPECIFIED BY OTHERS.

2 STANDARD DENSITY WALL MOUNTED WORK AREA OUTLET
CONFIGURATION



5 TYPICAL MAIN PDU UNIT WITH REAR DETAIL AND ADAPTORS REQUIRED FOR VERTICAL PDU




④ 110 Volt PDU FOR PLACEMENT AS NEEDED



APC AP8961 Rack PDU 2G,Switched, Zero U,5.7kW, 200/
208V,(21)C13 & (3)C19, 6' cord

REQUIRES ONE (1) L21-20R



BUS OR FEEDER

ZONE PDU

RACK MOUNT UPS

“ZERO U” VERTICAL PDU

DUAL POWER SUPPLY

2 NOTIONAL POWER SCHEMATIC FOR INFORMATION ONLY - NOT FOR CONSTRUCTION

NOTE:

THIS DESIGN PROVIDES DIVERSE POWER INPUTS FOR ACTIVE EQUIPMENT BY SPLITTING THE SOURCE POWER ACROSS TWO INPUTS ON THE ZONE PDU. EACH INPUT WILL SUPPORT TWO EQUIPMENT-FACING PDUs. EACH SERVER CABINET WILL CONTAIN A MINIMUM OF TWO EQUIPMENT-FACING PDUs - EACH WILL BE ENERGIZED BY SEPARATE ZONE PDU INPUTS.



1 POWER SCHEMATIC FOR POWER RACK- LEVEL REDUNDANCY



PROJECT:

CBOC ITS SPECIFICATIONS

PROJECT No:

N/A

<i>MARK</i>	<i>DATE</i>	<i>DESCRIPTION</i>

ISSUE:

DRAWING No:

FILE: CBOC INSIDE PLANT ITS SPEC V1.vsd

DRAWN BY: Kevin Grzelka

CHECKED BY: Michael Julian, RCDD

DOC VERSION No: 1.0

PRINT DATE: Oct 5, 2017

ISSUE DATE: Oct 5, 2017

SHEET TITLE

TYPICAL POWER DISTRIBUTION

T4 - TYPICAL RACK POWER DISTRIBUTION

SHEET: 11 OF 15



IT Operations and Services
Solution Delivery



PROJECT:

CBOC ITS
SPECIFICATIONS

PROJECT No:

N/A

MARK	DATE	DESCRIPTION
------	------	-------------

ISSUE:

DRAWING No:

FILE: CBOC INSIDE PLANT ITS SPEC V1.1.vsd

DRAWN BY: Kevin Grzelka

CHECKED BY: Michael Julian, RCDD

DOC VERSION No: 1.0

PRINT DATE: Oct 5, 2017

ISSUE DATE: Oct 5, 2017

SHEET TITLE

POWER DISTRIBUTION

T4 - POWER DISTRIBUTION

SHEET: 12 OF 15

APC AP8961 RACK PDU
2G, SWITCHED, ZERO-U, 5.7KW,
200/208V, (21)C13 & (3)C19, 6'
CORD

ZONEIT
30 Amp 3-Phase PDU BASE UNIT - FRONT
(ZONIT ZON-C-ZPDU1)
REQUIRES TWO 30 AMP 3-PHASE (WYE) CIRCUITS
WITH L21-30R RECEPTACLES
(OR EQUIVALENT)


L21-30P "A" SIDE
REQUIRES A 208V, 30A, THREE-PHASE WHIP,
TERMINATING IN A NEMA L21-30R LOCKING
RECEPTACLE. THE NEUTRAL CONDUCTOR SHOULD BE
UPSIZED ONE GAUGE TO MATCH THE UPSIZED
NEUTRAL CONDUCTORS IN THE ZONE PDU UNITS.

L21-30P "B" SIDE
REQUIRES A 208V, 30A, THREE-PHASE WHIP,
TERMINATING IN A NEMA L21-30R LOCKING
RECEPTACLE. THE NEUTRAL CONDUCTOR SHOULD BE
UPSIZED ONE GAUGE TO MATCH THE UPSIZED
NEUTRAL CONDUCTORS IN THE ZONE PDU UNITS

PDU BRACKET P/N:
OR-MM20PDUMB1D2W-B
(FOR OTRONICS RACK ONLY)

RACK-MOUNTED 5KW 208V UNINTERRUPTIBLE
POWER SUPPLY (UPS) WITH NEMA 20A L21-
20P INPUT AND L21-20R OUTPUT. MODEL
EXAMPLE: ZC0517700110000 5 KW 208V W/
20A 5W IN/5W OUT, ONE INTERNAL BATTERY
STRING

1 POWER SCHEMATIC RACKS - REAR VIEW

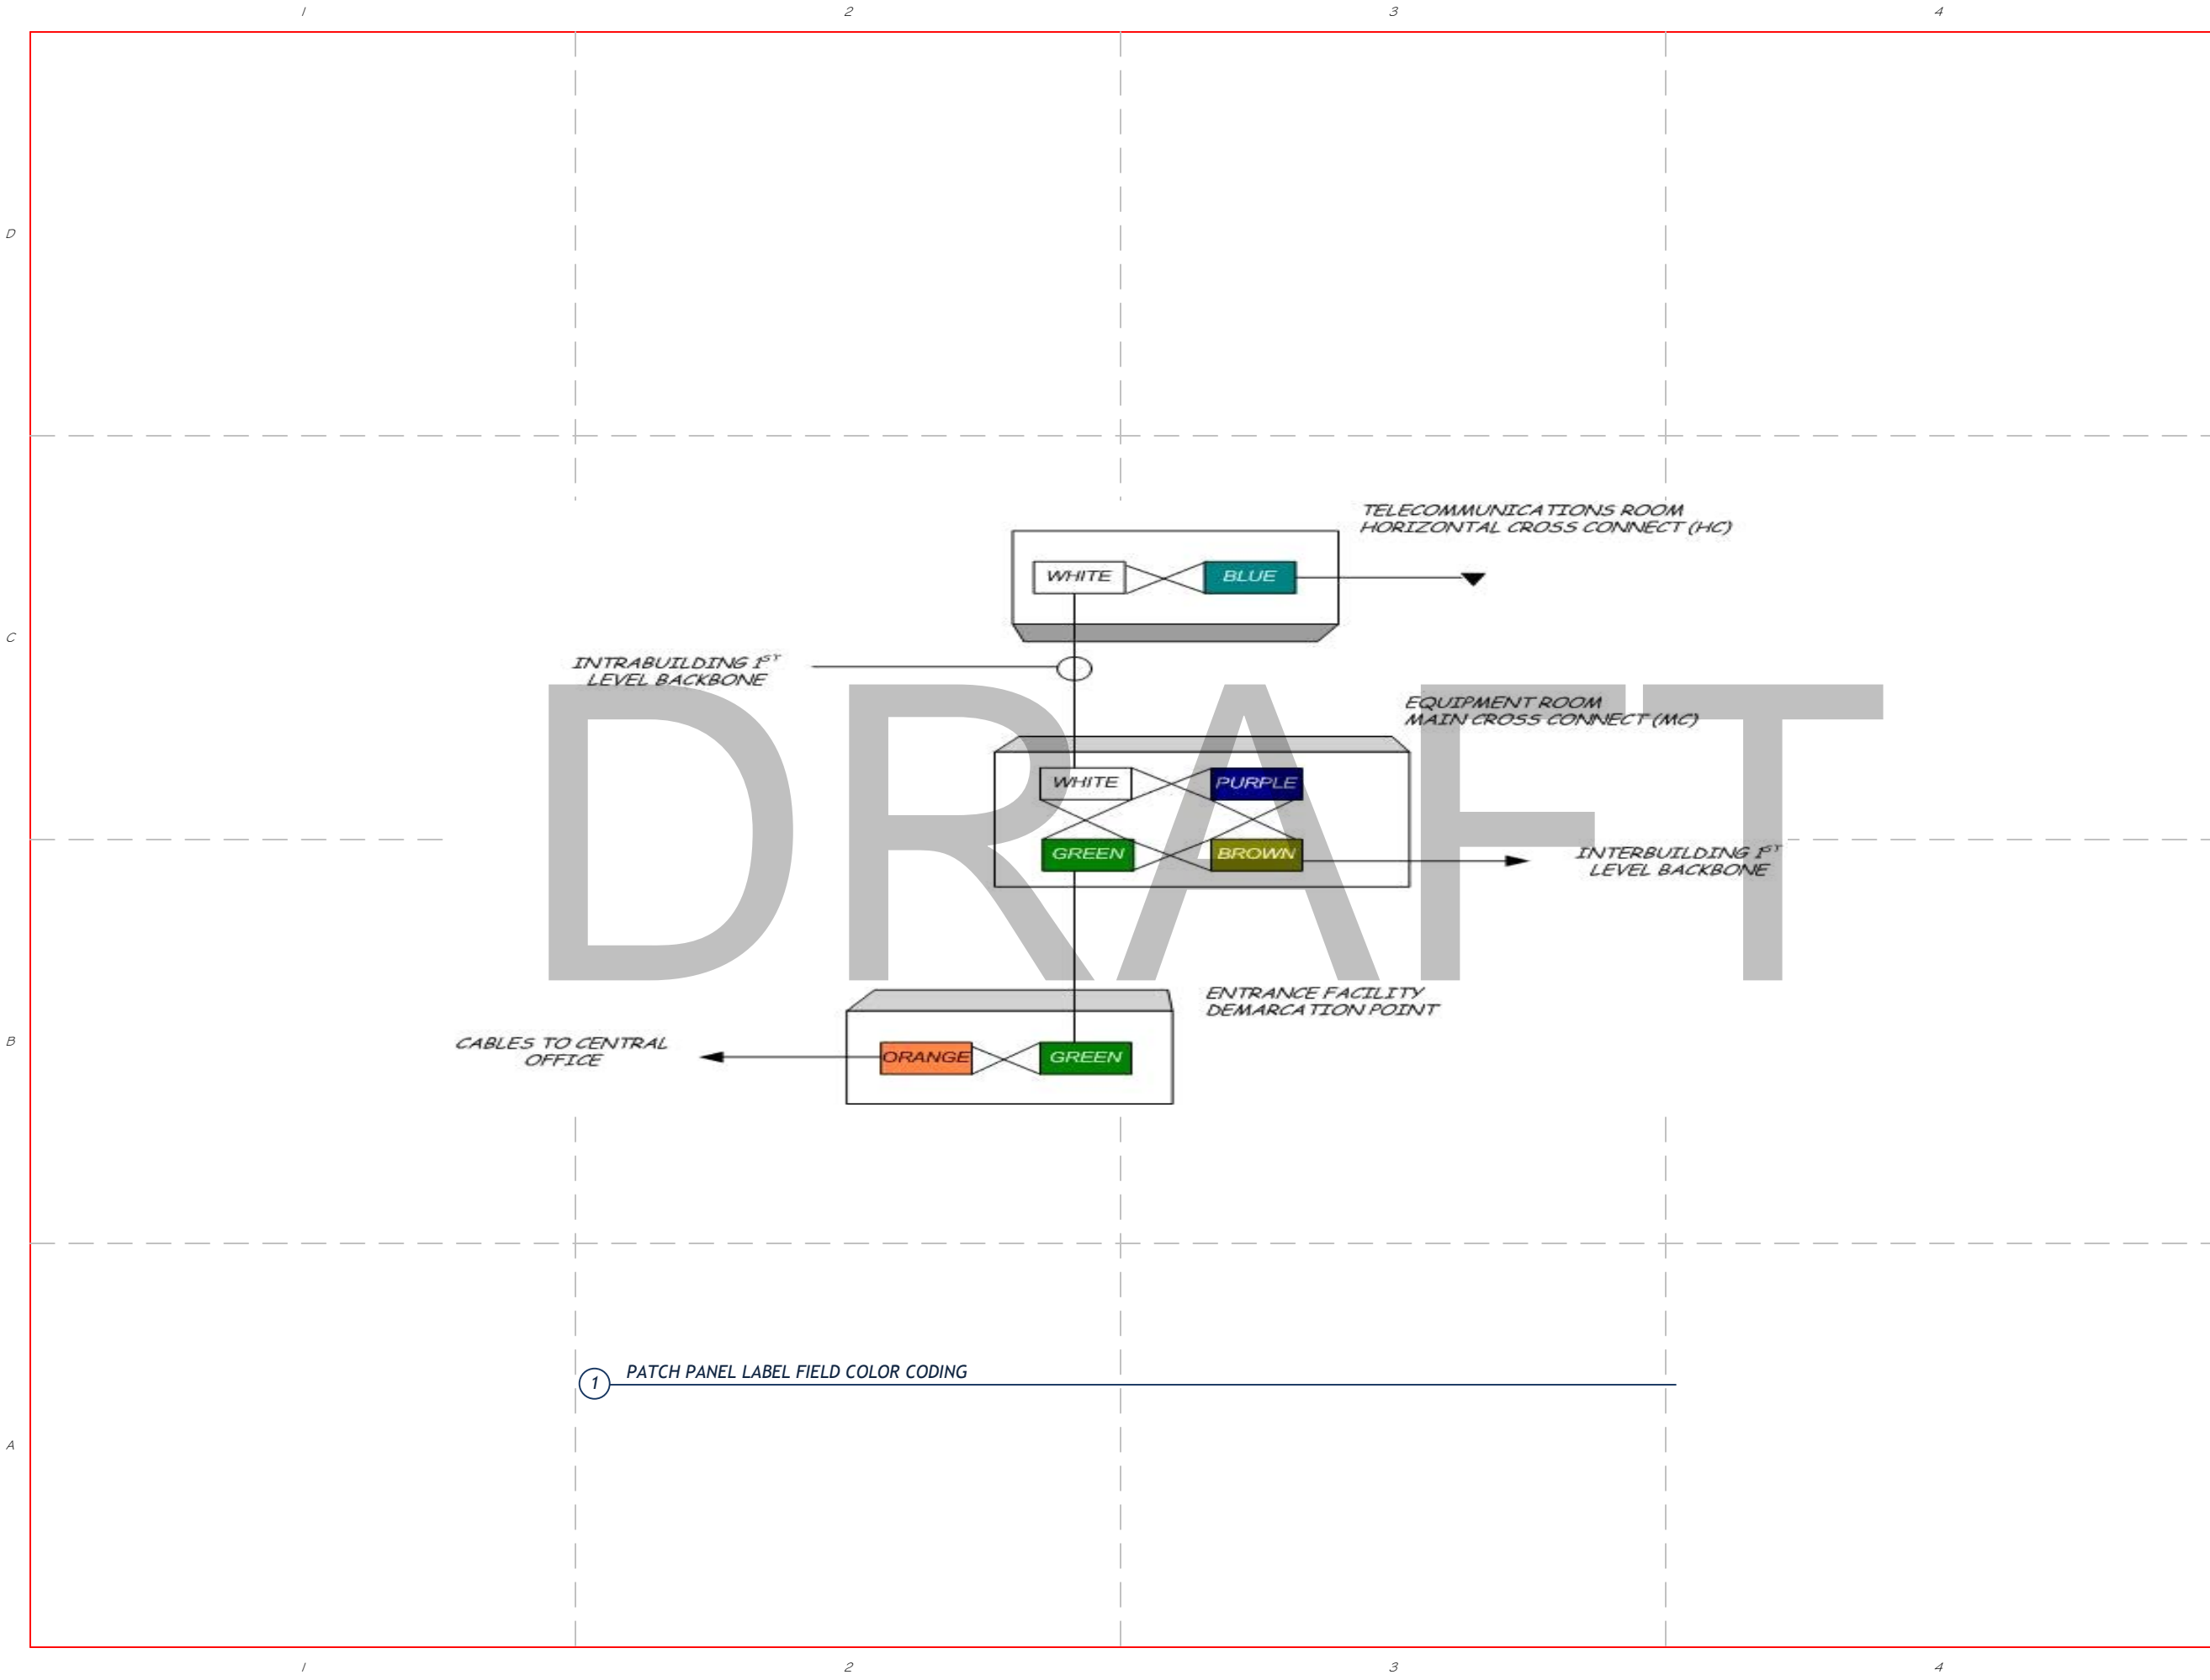

PROJECT:
CBOC ITS SPECIFICATIONS

PROJECT No:
N/A

MARK	DATE	DESCRIPTION

ISSUE:	
DRAWING No:	
FILE:	CBOC INSIDE PLANT ITS SPEC V1.1.vsd
DRAWN BY:	Kevin Grzelka
CHECKED BY:	Michael Julian, RCDD
DOC VERSION No:	1.0
PRINT DATE:	Oct 5, 2017
ISSUE DATE:	Oct 5, 2017
SHEET TITLE	

CBOC ITS SPECIFICATIONS

N/A

MARK	DATE	DESCRIPTION
------	------	-------------

ISSUE:

DRAWING No:

FILE: CBOC INSIDE PLANT ITS SPEC V1.vsd

DRAWN BY: Kevin Grzelka

CHECKED BY: Michael Julian, RCDD

DOC VERSION No: 1.0

PRINT DATE: Oct 5, 2017

ISSUE DATE: Oct 5, 2017

SHEET TITLE

T5 - CBOC ITS NAMING STANDARDS

SHEET: 14 OF 15

- **RACK** = RK1 THROUGH RK4. LABELED LEFT TO RIGHT WHEN LOOKING AT THE FRONT OF THE RACK. APPLIES TO RACKS AND CABINETS.
- **UTP PATCH PANEL** = CPL-RACK NAME-01 THROUGH 45. EXAMPLE: CPL-RK1-01 FOR THE PANEL LOCATED IN RACK UNIT #1 IN RACK #1.
- **UTP PATCH PANEL POSITION** = PANEL ID.01 THROUGH 24. EXAMPLE CPL-RK1-01.01
- **FIBER DISTRIBUTION PANEL** = FPL-RACK NAME-01 THROUGH 45. EXAMPLE: FPL-RK1-01 FOR THE PANEL IN RACK UNIT #1 RACK #1.
- **FIBER DISTRIBUTION CASSETTE** = FCS-RACK NAME-01 THROUGH 45.1 THROUGH 3. EXAMPLE: FCS-RK1-01.1 FOR THE CASSETTE IN POSITION #1 IN PANEL LOCATED IN RACK UNIT #1 IN RACK #1.
- **UTP PATCH CORDS** = CCA[SOURCE.PORT]/[DESTINATION.PORT]. EXAMPLE CCA[CPL-RK1-01.01]/[CPL-RK2-02.02] AS A PATCH CORD CONNECTING PORT #1 IN THE COPPER PATCH PANEL LOCATED IN RACK #1, RACK UNIT #1 WITH PORT 2 LOCATED IN RACK 2, RACK UNIT #2.
- **FIBER PATCH CORDS** = FCA[SOURCE.PORT]/[DESTINATION.PORT]. EXAMPLE FCA[FDP-RK1-01.01.01]/[FDP-RK2-02.02.02] AS A PATCH CORD CONNECTING PORT #1 IN THE FIBER PATCH PANEL LOCATED IN RACK #1, RACK UNIT #1 WITH PORT 2 LOCATED IN RACK 2, RACK UNIT #2.
- **FACEPLATE** = TR ROOM NUMBER-PATCH PANEL ID.PORT. EXAMPLE. 1A-CPL-RK1-01.1 FOR TELECOMMUNICATIONS ROOM 1, UTP PANEL IN RACK #1, RACK UNIT #1, PORT POSITION #1.

1 EXAMPLE INSIDE PLANT ADMINISTRATION

D	TELECOMMUNICATIONS MEDIA AND INTERFACES SPECIFICATION			D
	ID	PRIMARY ATTRIBUTE	SECONDARY ATTRIBUTE	SPECIFICATION
C	1	COPPER PATCH PANELS	PERFORMANCE CATEGORY	CATEGORY 6A (10 GBE)
			POSITION COUNT	24 (4 SIX-PORT MODULES)
			FORM FACTOR	ANGLED
			SIZE	ONE RACK UNIT
			COLOR CODING	BLACK
C	2	FIBER DISTRIBUTION CASSETTES	CASSETTE CAPACITY	24 STRAND (TWO 12-STRAND MULTI-FIBER PUSH ON (MPO))
			CASSETTE USER INTERFACES	LC QUAD CONNECTORS
			CASSETTE BACKBONE INTERFACES	MPO
			PERFORMANCE CHARACTERISTICS	OM4 LASER ENHANCED 40 GBE 50/125 MULTIMODE
			FORM FACTOR	ONE (1) RU
B	3	UTP (HORIZONTAL AND FIRST LEVEL BACKBONE)	PERFORMANCE CATEGORY	CATEGORY 6A (10 GBE)
			PERFORMANCE SPECIFICATIONS	MEETS OR EXCEEDS TIA-EIA-568-C.2-10, TSB-155.
			JACKET COLOR	BLUE (HORIZONTAL), WHITE (1 ST LEVEL BACKBONE)
			SIZE	ONE RACK UNIT
			COLOR CODING	BLACK
B	4	FIBER (HORIZONTAL AND FIRST LEVEL BACKBONE)	PERFORMANCE CATEGORY	OM4 LASER ENHANCED TO 40 GIGABIT ETHERNET (GBE
			PERFORMANCE SPECIFICATIONS	LASER OPTIMIZED 50/125 MM FIBERS WITH EFFECTIVE MODAL BANDWIDTH OF AT LEAST 4,700 MHZ·KM AT 850 NM
			MODE	MULTIMODE
				AQUA
			MEDIA CONNECTOR	PRE-TERMINATED WITH MPO, TYPE A
			STRAND COUNT	12
			BUNDLING	LOOSE TUBE
A	5	UTP PATCH CORDS	PERFORMANCE CATEGORY	CATEGORY 6A, 26-GAUGE, STRANDED
			PERFORMANCE SPECIFICATIONS	CENTER TUNED TO HORIZONTAL MEDIA
			JACKET COLOR	BLUE
			TERMINATION METHOD	FACTORY PRE-TERMINATED
	6	FIBER PATCH CORDS	PERFORMANCE CATEGORY	OM4 LASER ENHANCED TO 40 GIGABIT ETHERNET (GBE
			PERFORMANCE SPECIFICATIONS	OM4
			MODE	MULTIMODE
			JACKET COLOR	AQUA
			MEDIA CONNECTOR	PRE-TERMINATED WITH DUPLEX LC



PROJECT:
CBOC ITS SPECIFICATIONS
PROJECT No:
N/A

MARK	DATE	DESCRIPTION

ISSUE:

DRAWING No:

FILE: CBOC INSIDE PLANT ITS SPEC V1.vsd

DRAWN BY: Kevin Grzelka

CHECKED BY: Michael Julian, RCDD

DOC VERSION No: 1.0

PRINT DATE: Oct 5, 2017

ISSUE DATE: Oct 5, 2017

SHEET TITLE
