

LOAD SHARE NORTH

(Project # 654-15-557)

**Clarifications from
5/18/17 Job Walk**

Projected CATERPILLAR generator dimensions

- **15'-7" long**
- **6'-9" wide**
- **9'-1" tall**

Office trailer / Dumpster space

- **If the contractor does not currently occupy trailer space at the hospital, a space of up to 30' will be provided**
 - **Final location will be determined at Project Precon**
 - **Contractor is responsible for connecting to hospital power**
 - **The City of Reno has stopped issuing most permits for trailers/dumpsters on the street. Any coordination/negotiations with the City for trailer/dumpster permits are the responsibility of the contractor.**

BLDG 10

BUILDING 10

(E) BLDG. 10
ELECTRICAL ROOM

(E) BLDG. 10

Bridge construction
site (est. completion
Sept 2017)

(E) TRANSFORMER
T7
(E) CHAIN
LINK FENCE

(E) TEL

(E) EMH

8'-0"
CLEAR

(E) MH

7'-2" head clearance
under bridge

(E) GENERATOR
PAD

New bridge
between Bldg. 1/6

BUILDING 1 - WAREHOUSE EXPANSION

BUILDING 1


(E) BUILDING 1 NORTH

BLDG 1

(E) SMOKE
SHELTER


13
11
11
13
11

Yellow shaded area: Available laydown space for Load Share North project

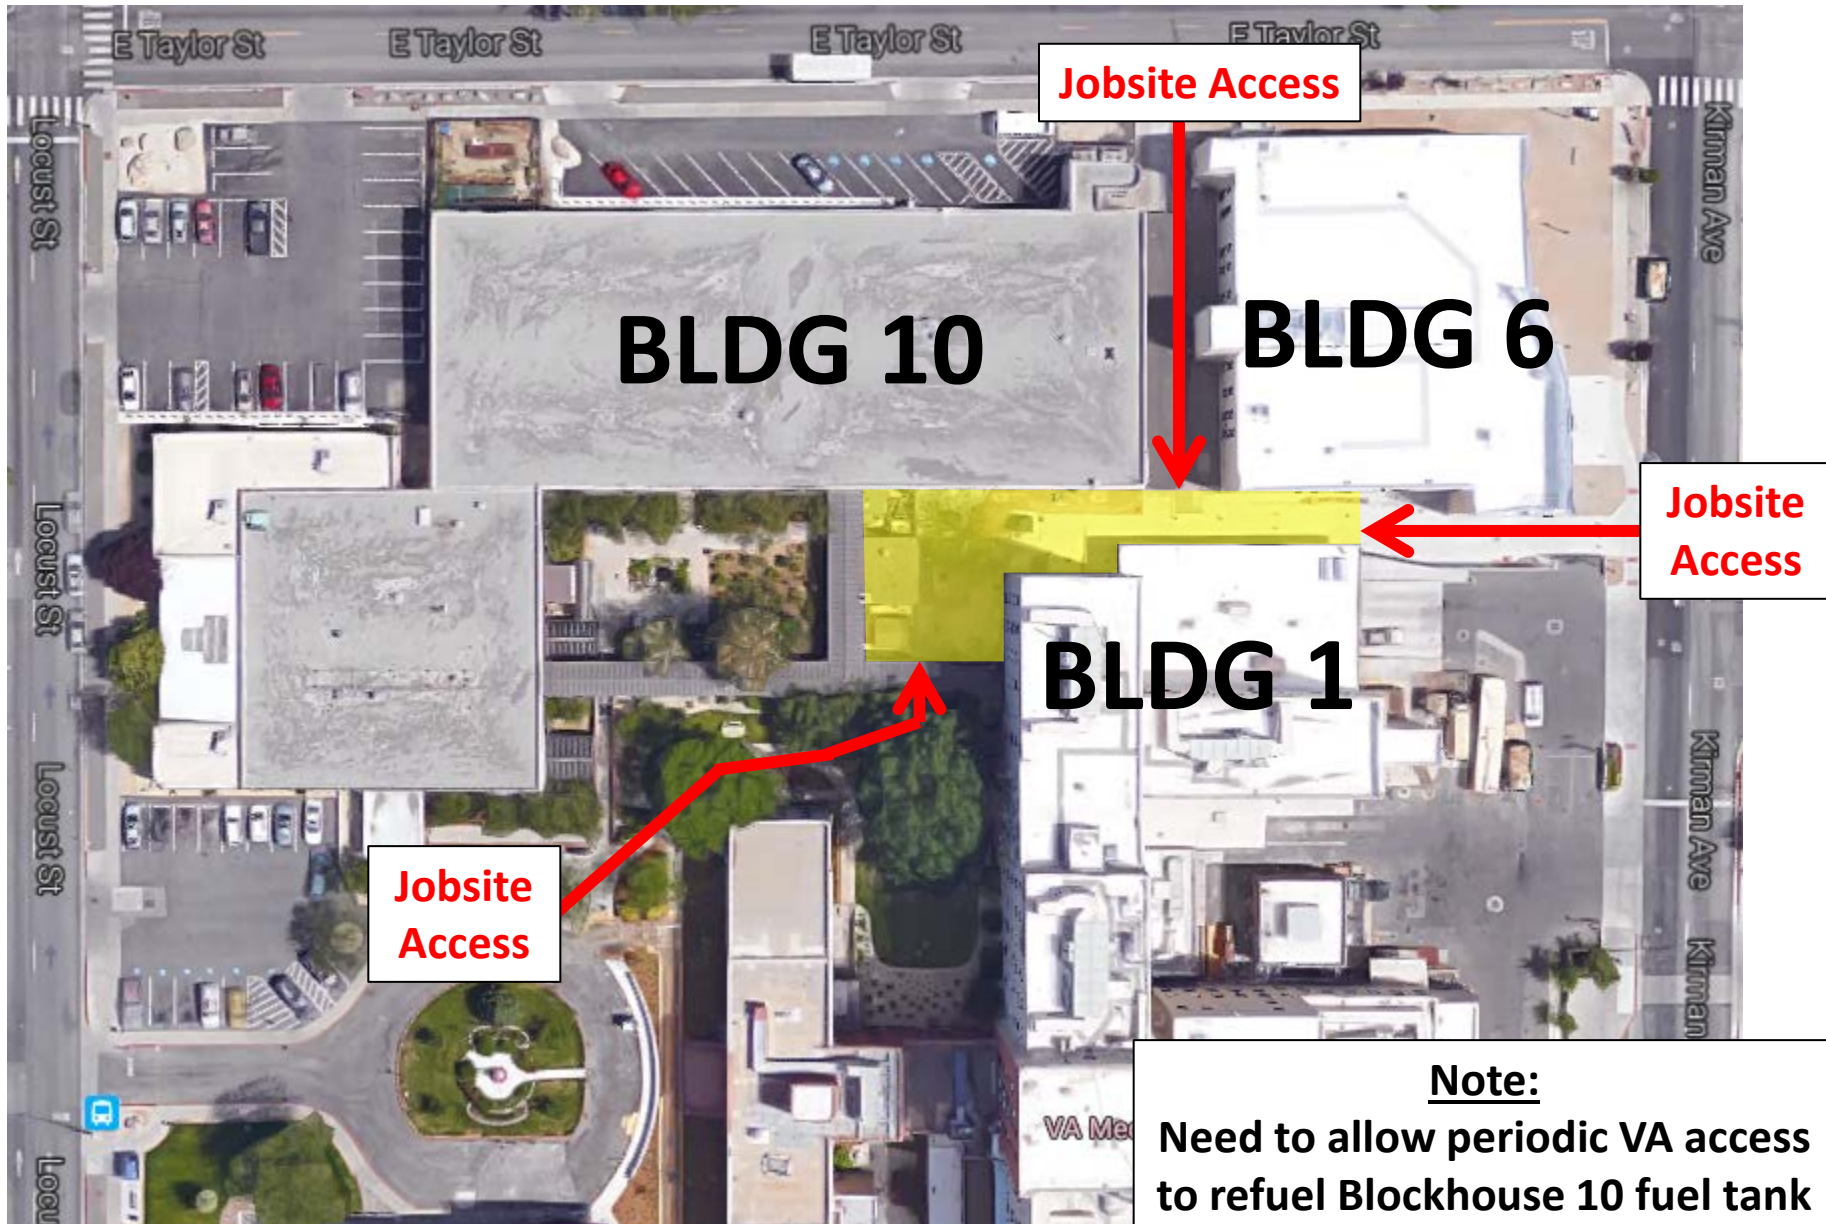

Blue shaded areas:

Locations acceptable to have suspended crane loads

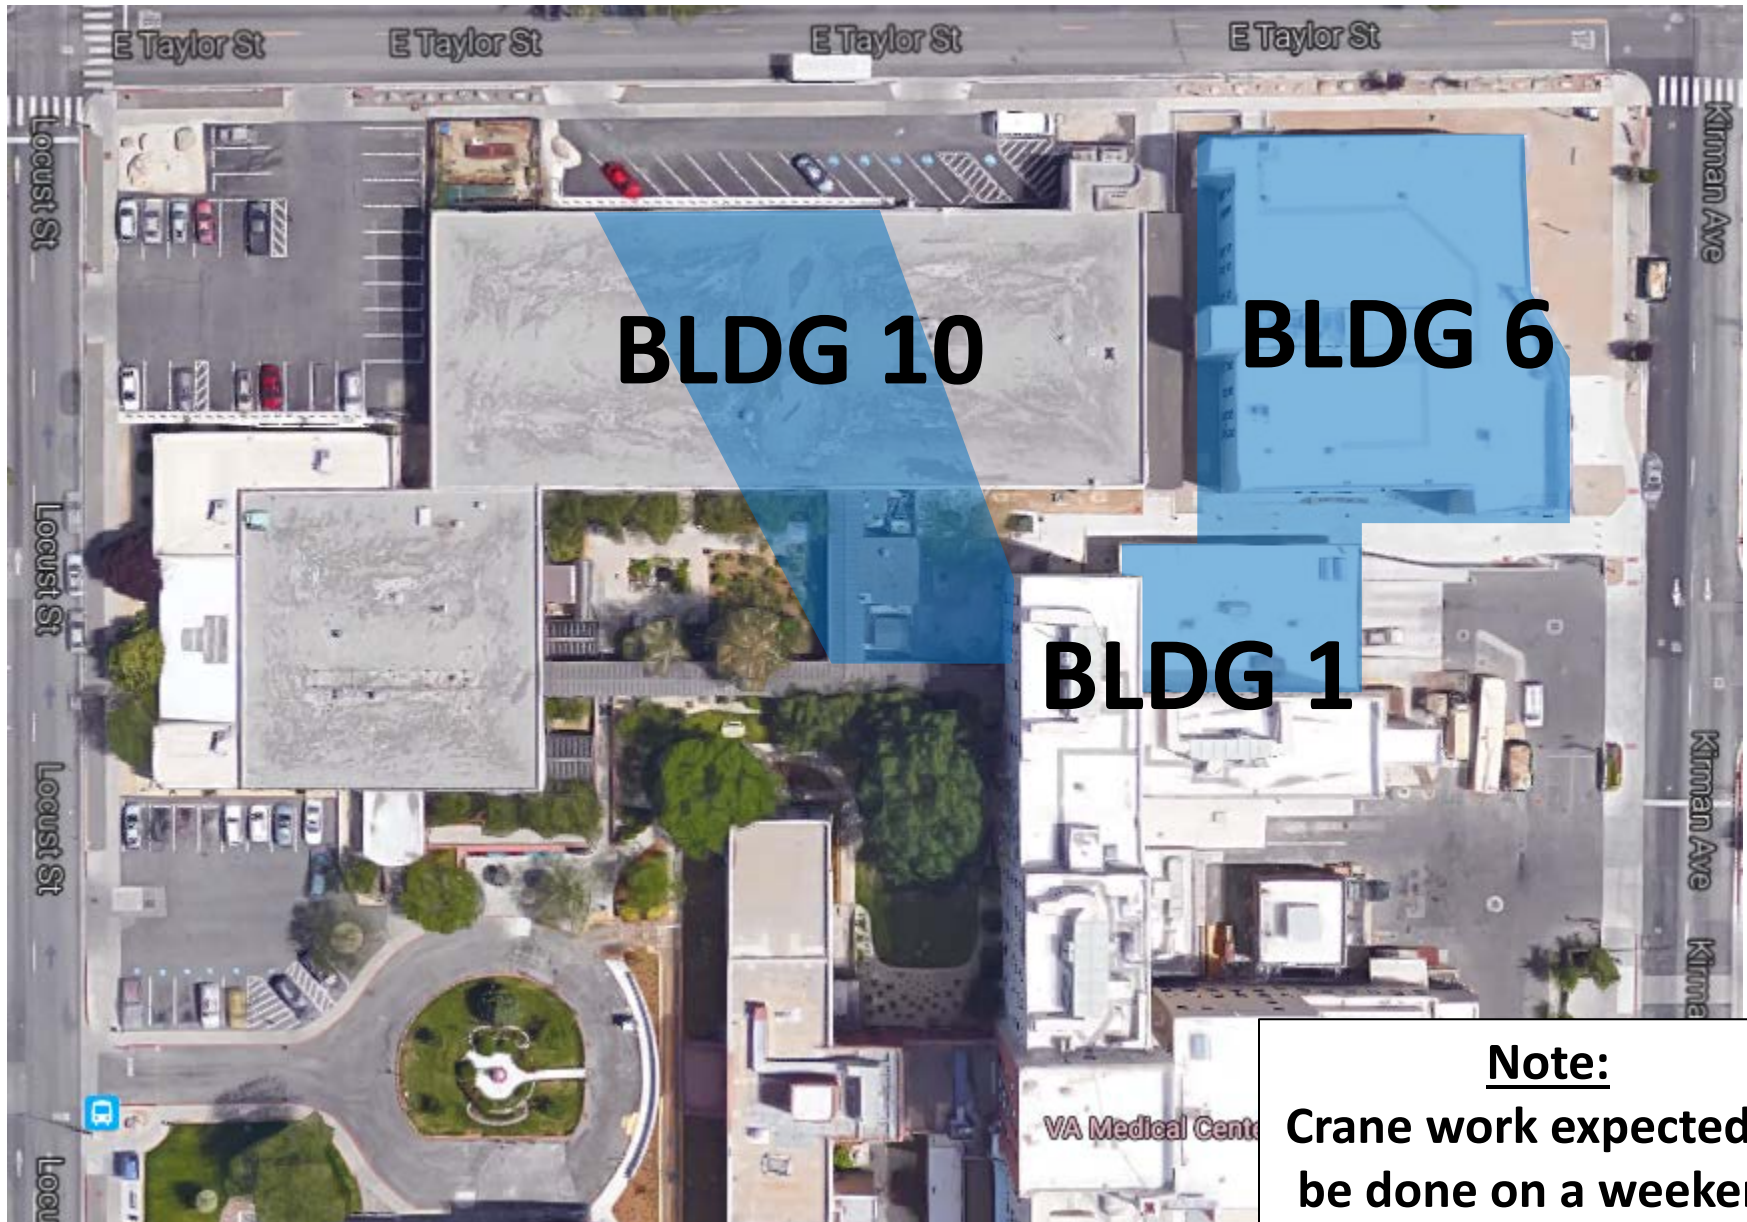

Note:

Crane work expected to be done on a weekend
