




EQUIPMENT DEMOLITION PLAN

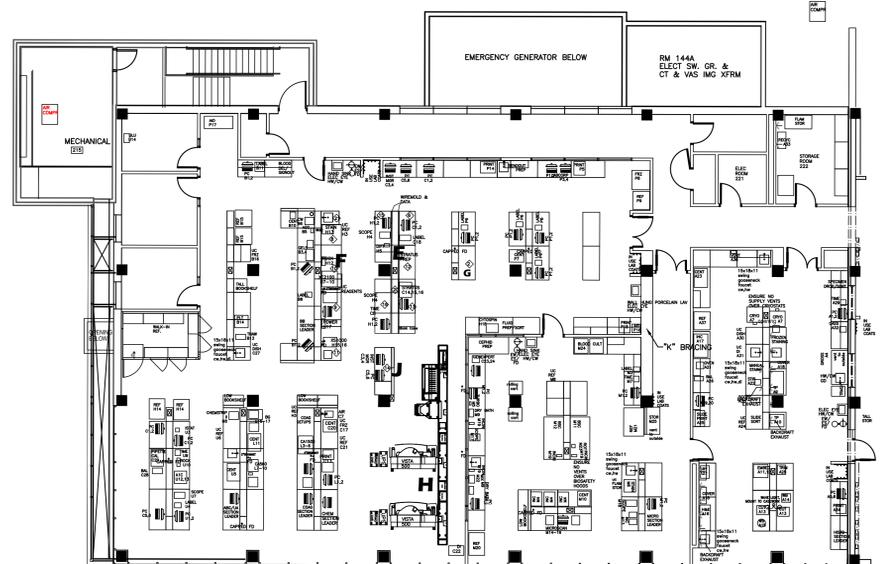

EQUIPMENT INSTALLATION/MOVE PLAN

**DEMOLITION WORK NOTES**

1. DEMO ISLAND 'A' WORK TO INCLUDE MOVING ALL LAB EQUIPMENT TO NEW ASSIGNED LOCATIONS. REMOVING ALL TABLES (12-17, 20 & 21), DISMANTLING THE UTILITY CHASE CABINETS, ELECTRICAL AND PLUMBING FOR RELOCATION.
2. DEMO LAB EQUIPMENT 'B' FOR STREAM LAB INSTALLATION AND MOVE LAB EQUIPMENT TO NEW ASSIGNED LOCATION. REMOVE TABLES (2, 7-11 & 18) AND ADJUSTING TABLES 22 & 23 AS REQUIRED. REMOVE ELECTRICAL AND PLUMBING (SALVAGE FOR REUSE) AS REQUIRED.
3. MOVE EQUIPMENT 'C' AND LAB DESKS (3-6) TO NEW ASSIGNED LOCATION. ELECTRICAL, PLUMBING, AND UTILITY CHASE TO REMAIN FOR INSTALLATION OF NEW EQUIPMENT AND TABLES. ADJUST WIREMOLD OUTLETS AND PLUMBING FOR NEW EQUIPMENT AS REQUIRED.
4. MOVE VISTA 500 ANALYZERS 'D', UPS UNITS, BATTERIES, AND ASSOCIATED CONTROLS TO NEW STREAM LAB UNIT. WORK TO INCLUDE RELOCATING ALL ELECTRICAL, MECHANICAL, PLUMBING, AND DATA LINES TO RECONNECT THE VISTA 500 ANALYZERS AT THE NEW STREAM LAB. PATCH AND REPAIR FLOORS, WALLS, AND CEILING AS REQUIRED.
5. MOVE EXCESS TABLES AND EQUIPMENT TO HOSPITAL LOADING DOCK FOR TRANSFER TO STORAGE.

**SHEET KEYNOTES**

- LOCATION OF EQUIPMENT TO BE MOVED FOR LAB DEMOLITION.
- ◇ LAB EQUIPMENT RE-INSTALLATION LOCATION.

**GENERAL NOTES**

1. ALL UNUSED EQUIPMENT AND LAB TABLES REMAIN GOVERNMENT PROPERTY.
2. THE CONTRACTOR IS RESPONSIBLE TO MOVE ALL UNUSED EQUIPMENT AND LAB TABLES TO THE HOSPITAL LOADING DOCK.
3. MOVING OF ALL EQUIPMENT AND LAB TABLES IS REQUIRED TO BE DONE IN PHASES AND COORDINATED WITH THE PROJECT ENGINEER AND LAB MANAGER.
4. THE CONTRACTOR IS RESPONSIBLE TO PATCH AND REPAIR ANY DAMAGE TO THE FLOORS, WALLS, OR CEILING CAUSED DURING THE MOVING AND INSTALLATION OF EQUIPMENT.
5. THE CONTRACTOR IS RESPONSIBLE TO PROTECT ALL ADJACENT EXISTING EQUIPMENT DURING THE RENOVATION.
6. THE CONTRACTOR IS REQUIRED TO RECONFIGURE AND ADJUST DRINKS OR SHELVEING ATTACHED TO LAB TABLES AS PART OF EQUIPMENT MOVES.
7. INSTALL OF ELECTRICAL, DATA AND PLUMBING LINES IN OCCUPIED OFFICES WILL HAVE TO BE DONE AFTER NORMAL WORKING HOURS.

**INSTALLATION WORK NOTES**

1. REINSTALL UTILITY CHASE CABINETS 'A' WITH ELECTRICAL, PLUMBING AND DATA AT LOCATION 'E'. VERIFY EQUIPMENT REQUIREMENTS PRIOR TO ROUGH-IN AND INSTALLATION OF UTILITY CHASE CABINETS AND LAB TABLES (6, 12, 13, 15, 16, 20).
2. RE-INSTALL SINK AND COUNTERTOP (21). INSTALL NEW DRAIN AND WATER LINES AS SHOWN AND CONNECT SINK AND FAUCET TO LINES. INSTALL LAB EQUIPMENT AND TABLES (6-11) AT LOCATION 'F'.
3. RE-INSTALL COMPUTER (2) AND PRINTER W/POWER & DATA CONNECTION LINES AT LOCATION 'G'.
4. STREAM LAB TO BE INSTALLED BY SIEMENS FACTORY REPRESENTATIVES.
5. EQUIPMENT, ASSOCIATED HARDWARE AND CONNECT TO NEW STREAM LAB AT LOCATION 'H'. TEST AND VERIFY ALL ELECTRICAL, PLUMBING, AND DATA LINES ARE OPERATING PROPERLY.
6. INSTALL STREAM LAB AIR COMPRESSOR IN ROOM 215 AND CONNECT TO NEW AIR LINE. PRESSURE REGULATOR AND AIR FILTER SYSTEM. TEST AND VERIFY COMPRESSOR OPERATION IS WORKING CORRECTLY. VERIFY LOCATION PRIOR TO ROUGH-IN.
7. INSTALL TABLE 14 AT LOCATION 'J' WITH NEW DATA AND ELECTRICAL CIRCUITS IN WIREMOLDING W/POWER POLE FEED. MOVE INSTRUMENT MANAGER COMPUTER FROM TABLE 3 AND RECONFIGURE POWER AND DATA LINES AS REQUIRED AT TABLE 14. TEST AND VERIFY COMPUTER OPERATION FOR STREAM LAB.

# VA MONTANA HEALTHCARE SYSTEM FT HARRISON, MT

REVISIONS2	REV-DATE-2
REVISIONS1	REV-DATE-1
Revisions	Date

Drawing Title <b>EQUIPMENT MOVE PLANS</b>		Project Title <b>LABORATORY TRACK SYSTEM SITE PREPARATION</b>		Date 6/8/2018
Approved Division Chief	Building Number 54	Checked	Drawn RJB	Project No. 498-0-8LP-01
Approved Service Director	Location			DRAWING NO. A 11
				Dwg 2 of 8

VA FORM 08-620, FEB 1983

DEPARTMENT OF VETERANS AFFAIRS
