


VISN 23 RF ROOM UPDATES

St. Cloud VA Health Care System

Staging and Parking Areas for Contractor Use

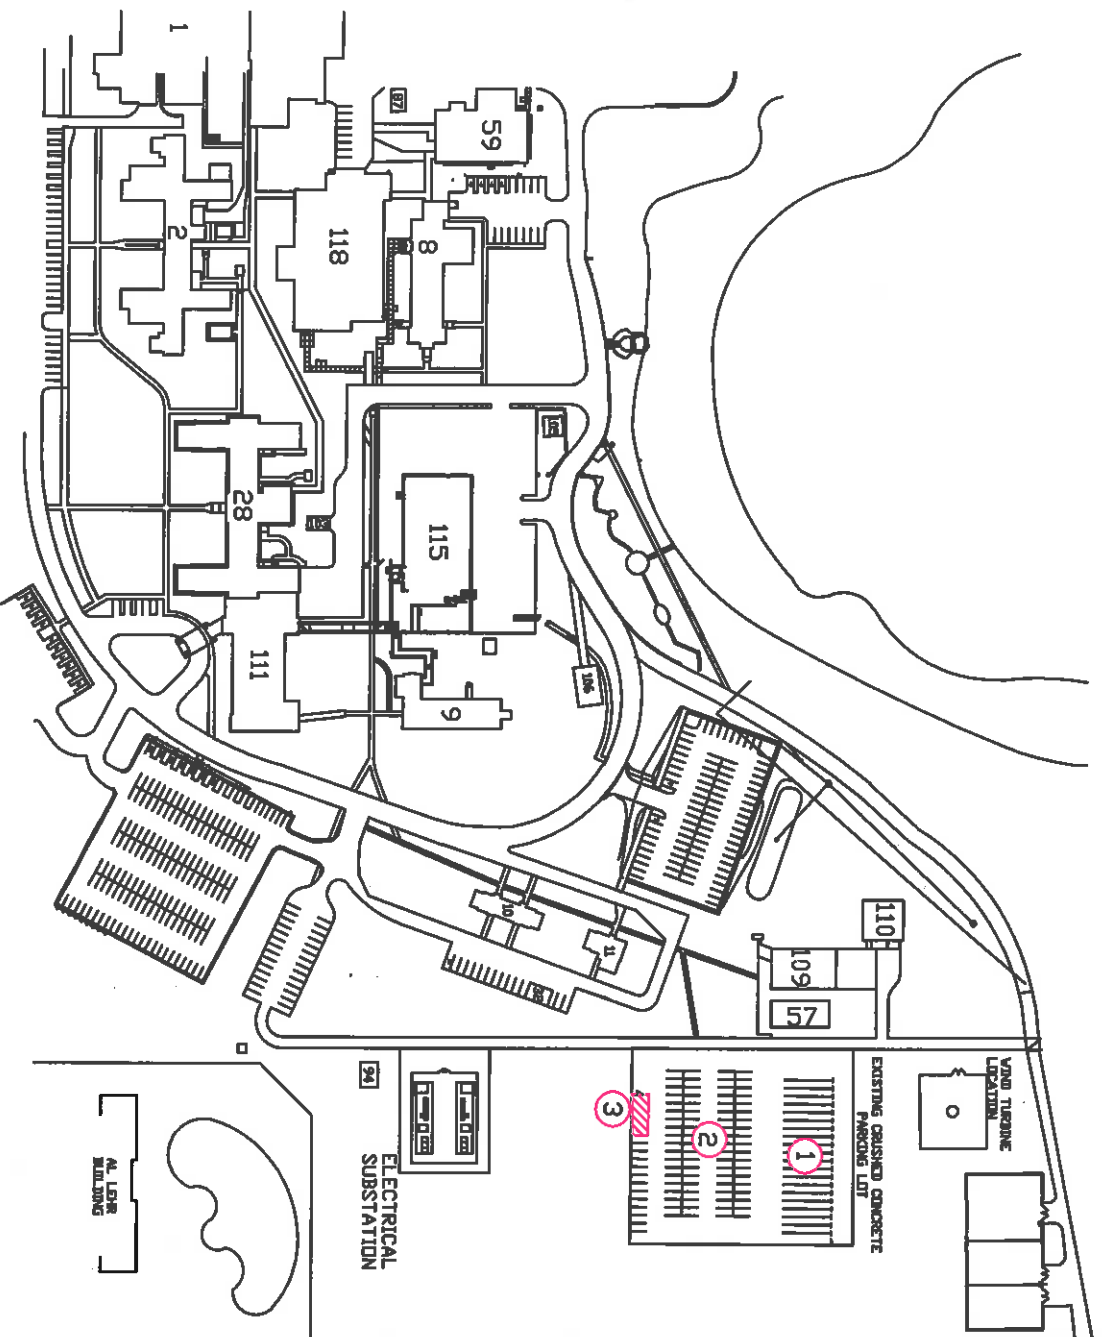

- 1 Contractor will be assigned one semi-trailer stall for parking an enclosed trailer for storage during construction.
- 2 Contractor will be allowed up to 5 permits for vehicle parking in this lot during construction.
- 3 Contractor may use up to 20x30' area for staging. All dumpsters used on the site shall be enclosed and staged within this area.
- 7' high chain link fencing with gates will be required for use. Installed with surface supports with sandbag or weights. Gates must be locked (chained) with padlock provided by VA. Area must be fully restored prior to project final inspection. Coordinate final layout with Saint Cloud Technical Monitor.

