



BOTTOM RAIL, 4"
6063-T6




MUNTIN BAR, 2"
6063-T6




STILE, NARROW
6063-T6


TRANSOM VERTICAL section not selected in the package



PANEL GLAZING SECTIONS
1/4" GLASS

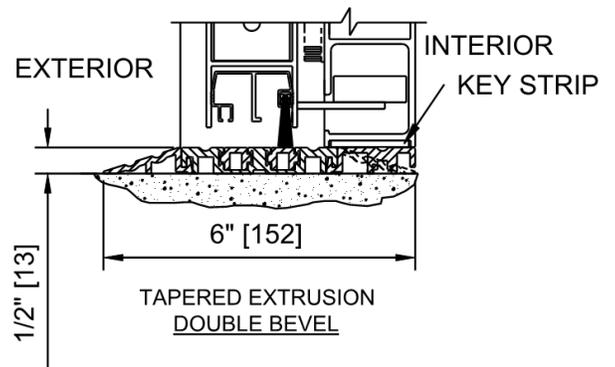

THRESHOLD-TAPERED EXTRUSION
4 1/2" FRAME
(DOUBLE BEVEL THROUGHOUT DOOR OPENING)



JAMB, 4 1/2"
6063-T6



Job Name : VA Primary Care Myrtle Beach
Location :
Door Location : Exterior

Job# : 142097
Product Qty : 1
Product : DURAGLIDE 2000 BP

Date: Feb 16 2018

Door Details

Package Width	Masonry/Rough Opening Width	Clear Door Opening Width	Emergency Breakout	Package Height	Rough Opening Height
144.0000"	144.5000"	60.3020"	67.5520"	90.0000"	90.2500"

Options	Inclusions/Exclusions
<p><u>Finish</u> Door Package Color Dark Bronze Anodized</p> <p><u>Locking / Access Control</u> Cylinder Options Standard Lock Configuration Cylinder/Thumbturn Required Lock Config Options Two Point Lock</p> <p><u>Options and Accessories</u> Jamb Substitution No Substitution Threshold Option Double Bevel 6" (Continuous) Switch Type Rotary Switch - 6 Position</p> <p><u>Glass Specifications</u> SX Glass Thickness 0.2500" O Glass Thickness 0.2500"</p>	<p><u>Inclusions</u> Door package installation. Demolition of existing storefront. 120 volts AC to inside auto door header 5 amp min. Glass & Glazing. Break metal. Caulking.</p> <p><u>Exclusions</u> Recess prep & grout for track or threshold. Painting, patching & flooring work. After hours premium labor. Delegated Design. Structural Review (no seismic review). Permits & inspections by others. Prevailing Wage. Certified Payroll. Cleaning and protection of installed material.</p>

Shop Drawing / Submittal Review


Date: _____

- No Exceptions Taken
 Furnish with Changes Noted
 Review and Resubmit
 Rejected


SUBMITTAL WAS REVIEWED FOR GENERAL CONFORMANCE TO THE CONTRACT DOCUMENTS. THE GENERAL CONTRACTOR IS RESPONSIBLE FOR CONFIRMING AND CORRELATING DIMENSIONS AT JOBSITE FOR TOLERANCE, CLEARANCE, QUANTITIES, FABRICATION, TECHNIQUES OF CONSTRUCTION, COORDINATION OF THIS WORK WITH THE WORK OF OTHER TRADES, AND FULL COMPLIANCE WITH THE CONTRACT DOCUMENTS.

By: _____


Company: _____

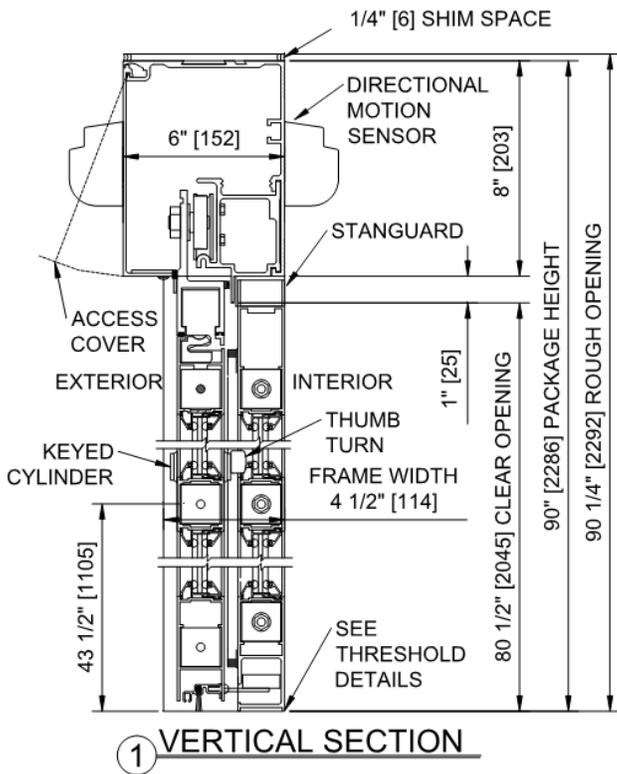


1 VERTICAL SECTION

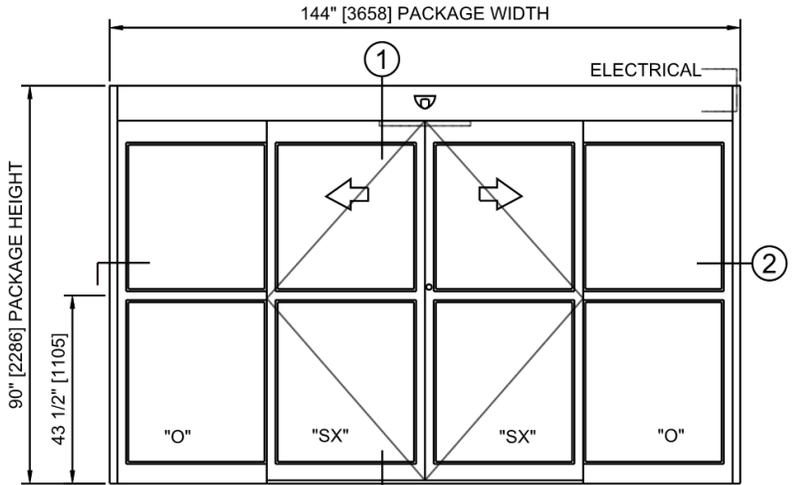

ELEVATION VIEW

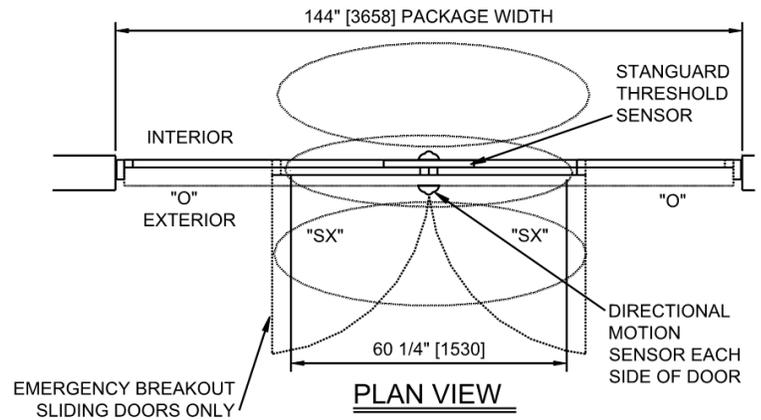

PLAN VIEW

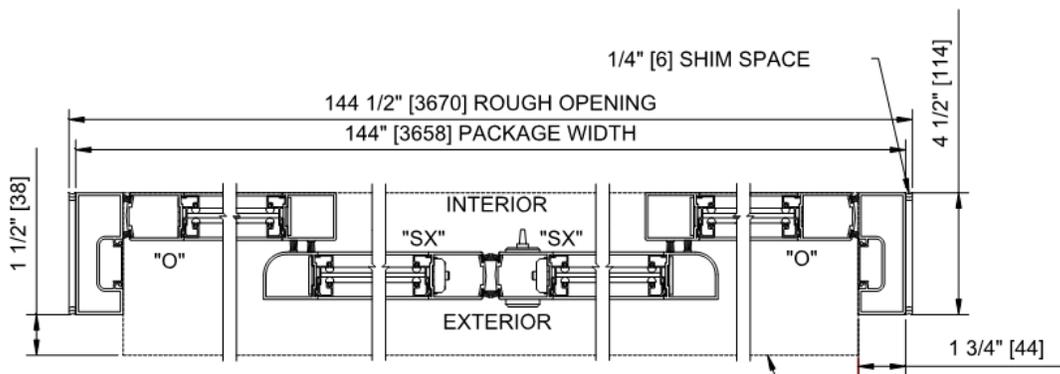


2 HORIZONTAL SECTION

STANLEY.


Job Name : VA Primary Care Myrtle Beach
Location :
Door Location : Interior

Job# : 142097
Product Qty : 1
Product : DURAGLIDE 2000 BP


Date: Feb 16 2018

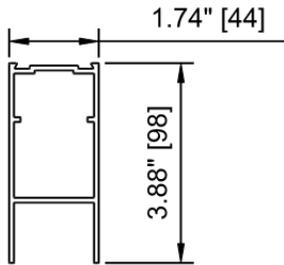

BOTTOM RAIL, 4"
6063-T6




MUNTIN BAR, 2"
6063-T6




STILE, NARROW
6063-T6


TRANSOM VERTICAL section not selected in the package



PANEL GLAZING SECTIONS
1/4" GLASS

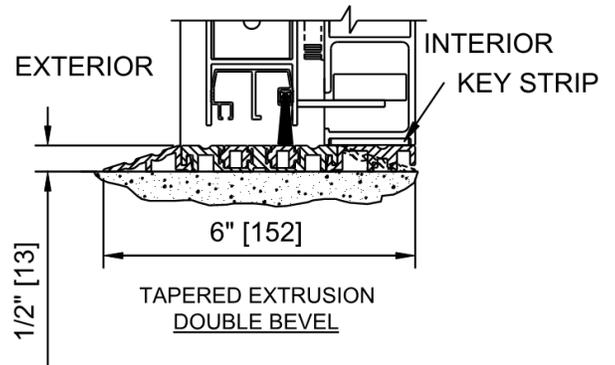

THRESHOLD-TAPERED EXTRUSION
4 1/2" FRAME
(DOUBLE BEVEL THROUGHOUT DOOR OPENING)



JAMB, 4 1/2"
6063-T6



Job Name : VA Primary Care Myrtle Beach
Location :
Door Location : Interior

Job# : 142097
Product Qty : 1
Product : DURAGLIDE 2000 BP

Date: Feb 16 2018

Door Details

Package Width	Masonry/Rough Opening Width	Clear Door Opening Width	Emergency Breakout	Package Height	Rough Opening Height
144.0000"	144.5000"	60.3020"	67.5520"	90.0000"	90.2500"

Options	Inclusions/Exclusions
<p><u>Finish</u> Door Package Color Dark Bronze Anodized</p> <p><u>Locking / Access Control</u> Cylinder Options Standard Lock Configuration Cylinder/Thumbturn Required Lock Config Options Two Point Lock</p> <p><u>Options and Accessories</u> Jamb Substitution No Substitution Threshold Option Double Bevel 6" (Continuous) Switch Type Rotary Switch - 6 Position</p> <p><u>Glass Specifications</u> SX Glass Thickness 0.2500" O Glass Thickness 0.2500"</p>	<p><u>Inclusions</u> Door package installation. Demolition of existing storefront. 120 volts AC to inside auto door header 5 amp min. Glass & Glazing. Break metal. Caulking.</p> <p><u>Exclusions</u> Recess prep & grout for track or threshold. Painting, patching & flooring work. After hours premium labor. Delegated Design. Structural Review (no seismic review). Permits & inspections by others. Prevailing Wage. Certified Payroll. Cleaning and protection of installed material.</p>

Shop Drawing / Submittal Review

Date: _____

- No Exceptions Taken
 Furnish with Changes Noted
 Review and Resubmit
 Rejected

SUBMITTAL WAS REVIEWED FOR GENERAL CONFORMANCE TO THE CONTRACT DOCUMENTS. THE GENERAL CONTRACTOR IS RESPONSIBLE FOR CONFIRMING AND CORRELATING DIMENSIONS AT JOBSITE FOR TOLERANCE, CLEARANCE, QUANTITIES, FABRICATION, TECHNIQUES OF CONSTRUCTION, COORDINATION OF THIS WORK WITH THE WORK OF OTHER TRADES, AND FULL COMPLIANCE WITH THE CONTRACT DOCUMENTS.

By: _____

Company: _____
