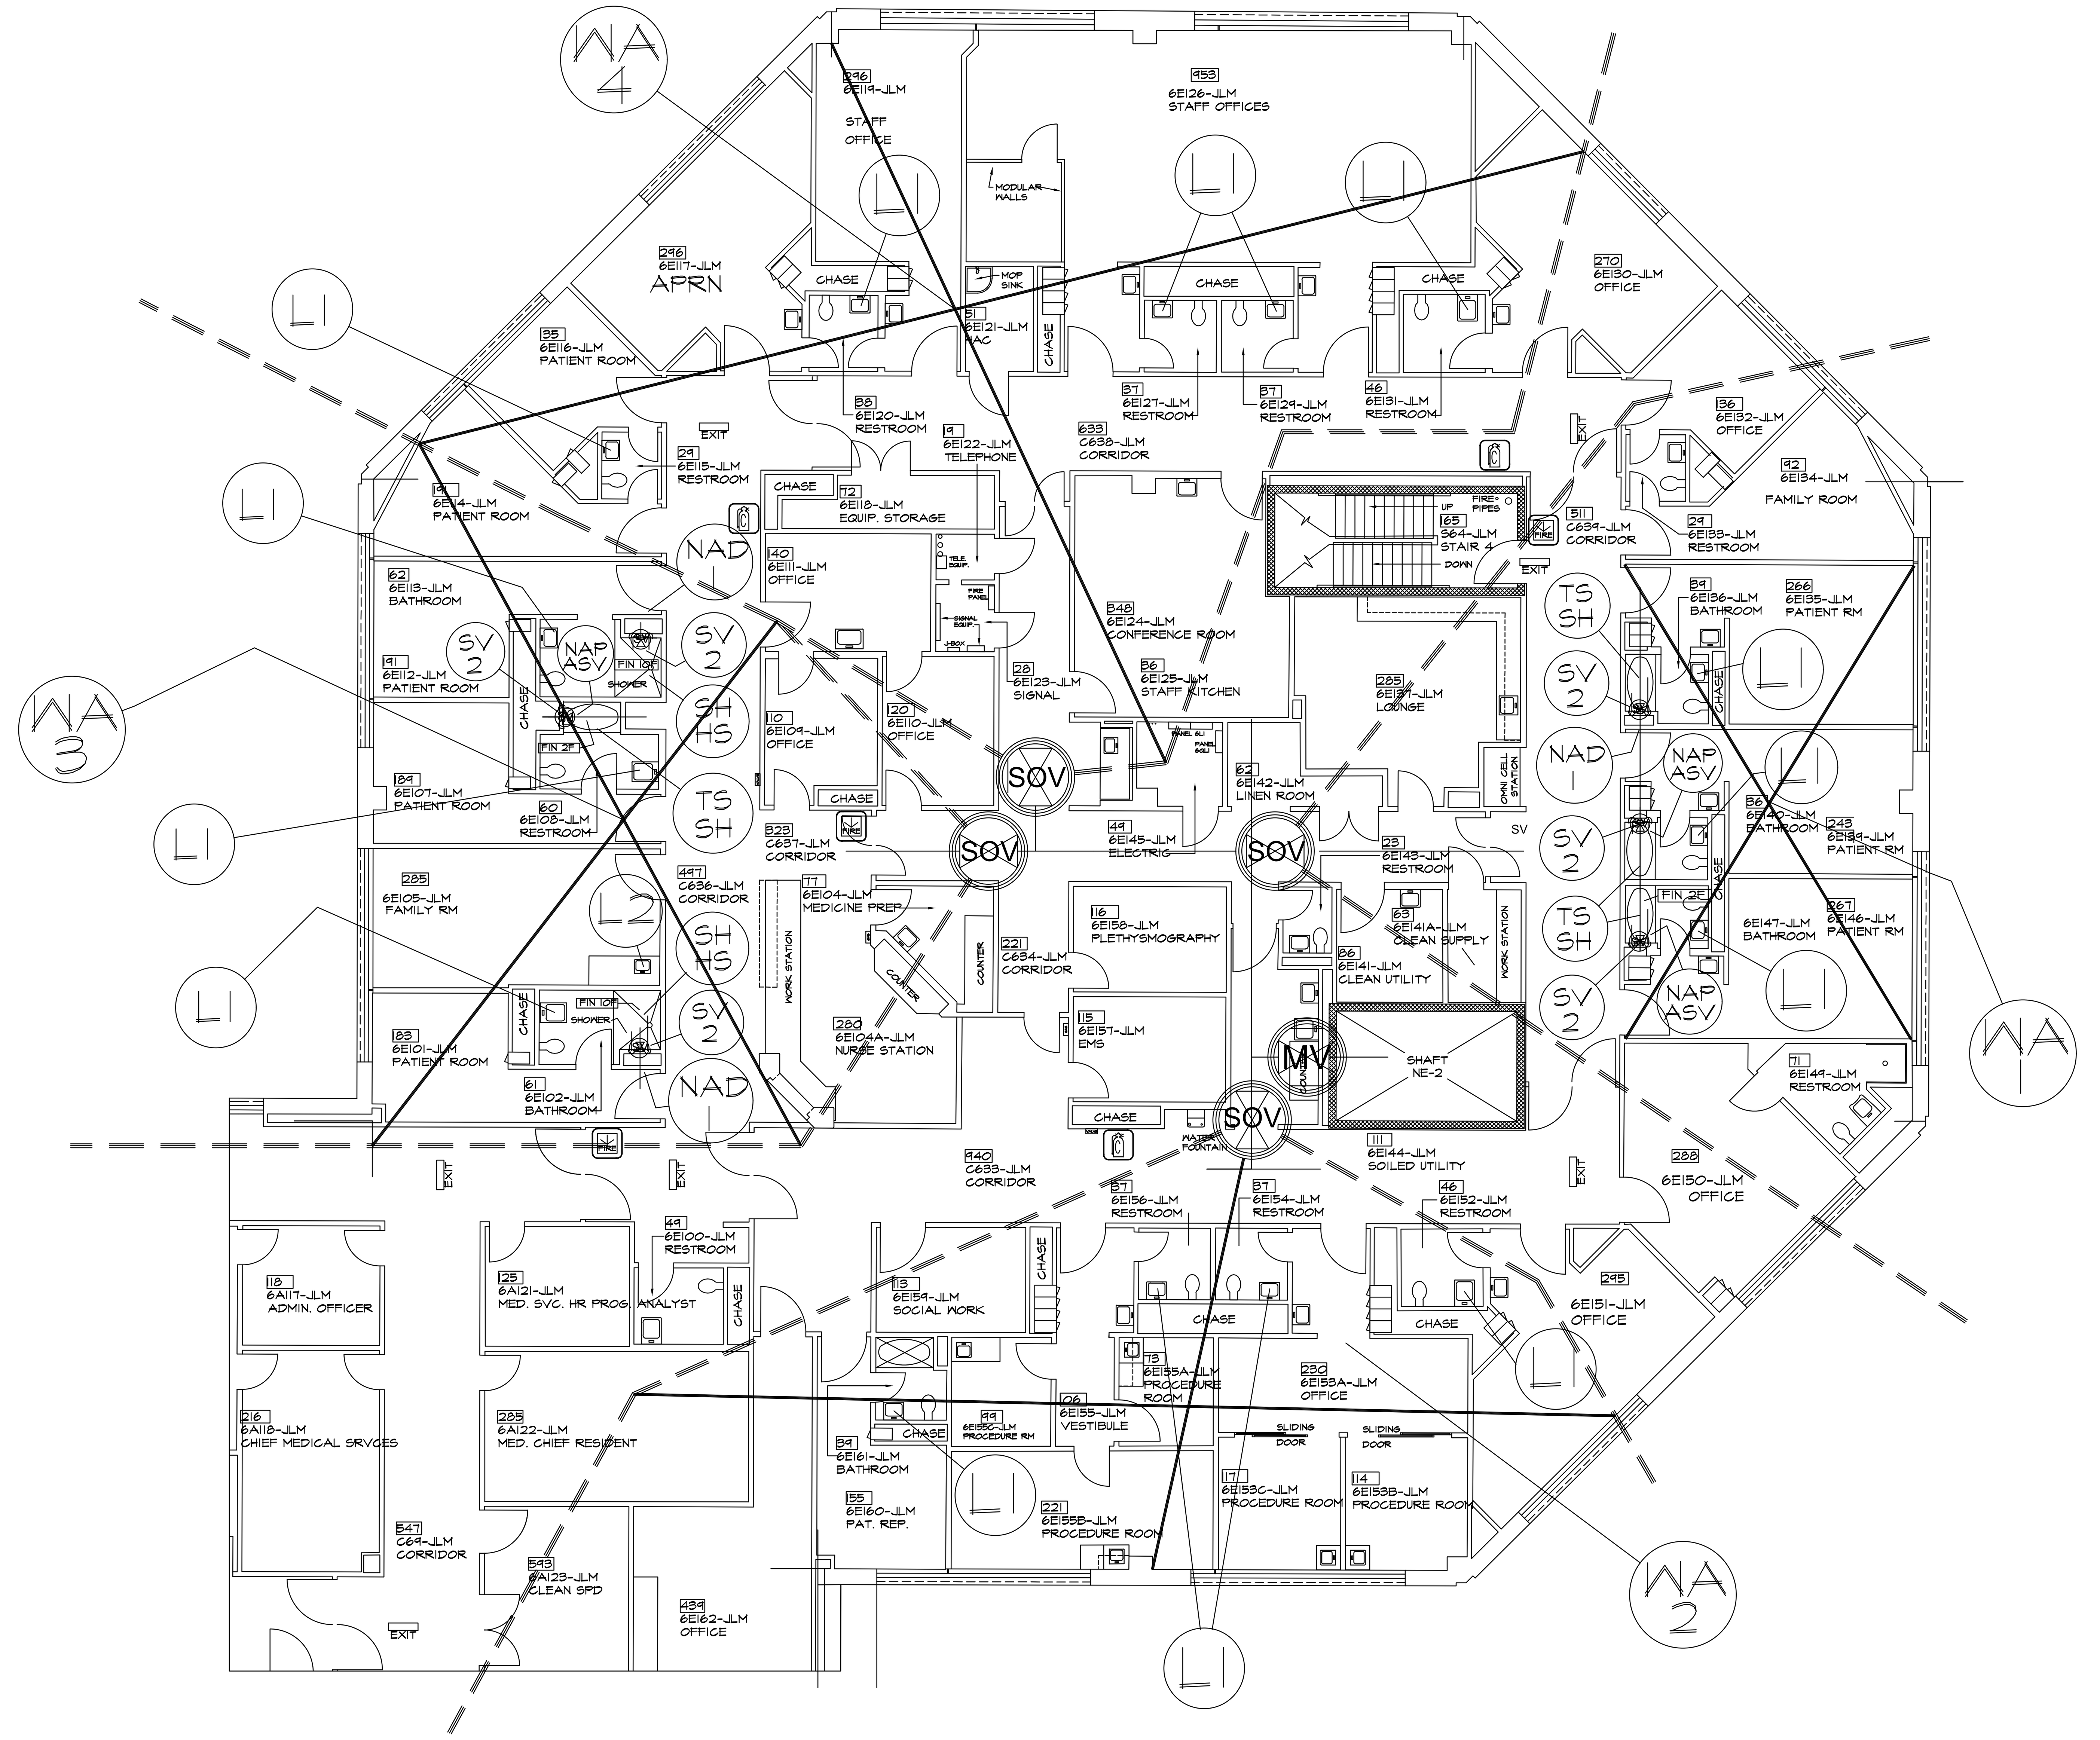

LR POD 6E - SHUT-OFF VALVES-ZONES-WORK AREAS

SCALE: 1/8" = 1'-0"

SYMBOLS:	
SOV	EXIST SHUT OFF VALVE AND AREA OF CONTROL. EXIST HW, CW, HWR, SHUT OFF VALVES ABOVE CEILING.
	AREAS OF WORK, TO BE SCHEDULED WITH USERS.
WA 1	WORK AREA AFFECTS 3 PAT BEDRMS 3 PATIENT TOILETS 3 TUB SHOWERS 3 PATIENT LAVS
WA 2	WORK AREA AFFECTS 4 PAT TOILETS 4 PATIENT LAVS
WA 3	WORK AFFECTS 3 PATIENT BEDRMS. 3 PATIENT TOILETS 4 PATIENT LAVS 1 TUB SHOWER 2 HA SHOWERS
WA 4	WORK AFFECTS 2 PATIENT BEDRMS. 1 PATIENT TOILET. 5 PATIENT LAVS
SOV CW HW HWR PIPE SIZES VARY	EXISTING TYPICAL ZONE SHUT OFF VALVES, LOCATED ABOVE CEILING. CW, HW, GATE AND COMB GATE, BAL VALVE FOR RECIRCULATE PIPING.

REFER TO SPECIFICATIONS FOR INFECTION CONTROL PROCEDURES.
REFER TO SPECIFICATION 01 32 16 FOR SCHEDULING OF WORK, AND PHASING.
IN GENERAL WORK SHALL BE SCHEDULED INDIVIDUALLY FOR EACH OF THE WORK AREAS SHOWN.
WHICH ARE VALVED ZONED AREAS.
EACH ZONE AREA SHALL BE COMPLETED SEPERATLY TO ALLOW MOVEMENT OF PATIENTS OUT OF THE RMS INSTALLATION OF THE WORK, INSPECTION, TESTING AND STERILIZATION & ACCEPTANCE OF TEST RESULTS & STERILE CLEANING OF THE AREAS, AND RE-OCCUPING.
COMPLETE EACH ZONE BEFORE MOVING TO THE NEXT.

PATIENTS WILL BE RELOCATED FROM AFFECTED BEDRMS WITHIN A ZONE
TO AVAILABLE BED SPACE ON THIS POD & TO OTHER PODS AS NECESSARY, FOR THE DURATION OF THE WORK IN THE AFFECTED WORK AREA.

NOTE SPECIFICATION REQUIREMENTS FOR CLEANING AND DISINFECTION OF NEW AND EXISTING PIPING AFTER NEW SHOWER VALVES ARE INSTALLED.
PATIENTS WILL BE VACATED AS NOTED ABOVE AND RETURNED TO RMS AFTER WORK IS COMPLETED.

287 — RM AREA
6E134-JLM — RM NO.
BEDROOM — RM TITLE

ROOM TITLE DESCRIPTOR

WORK AREAS

POD 6E
LR-B1-JLM
SCHEDULE
OF WK DWG

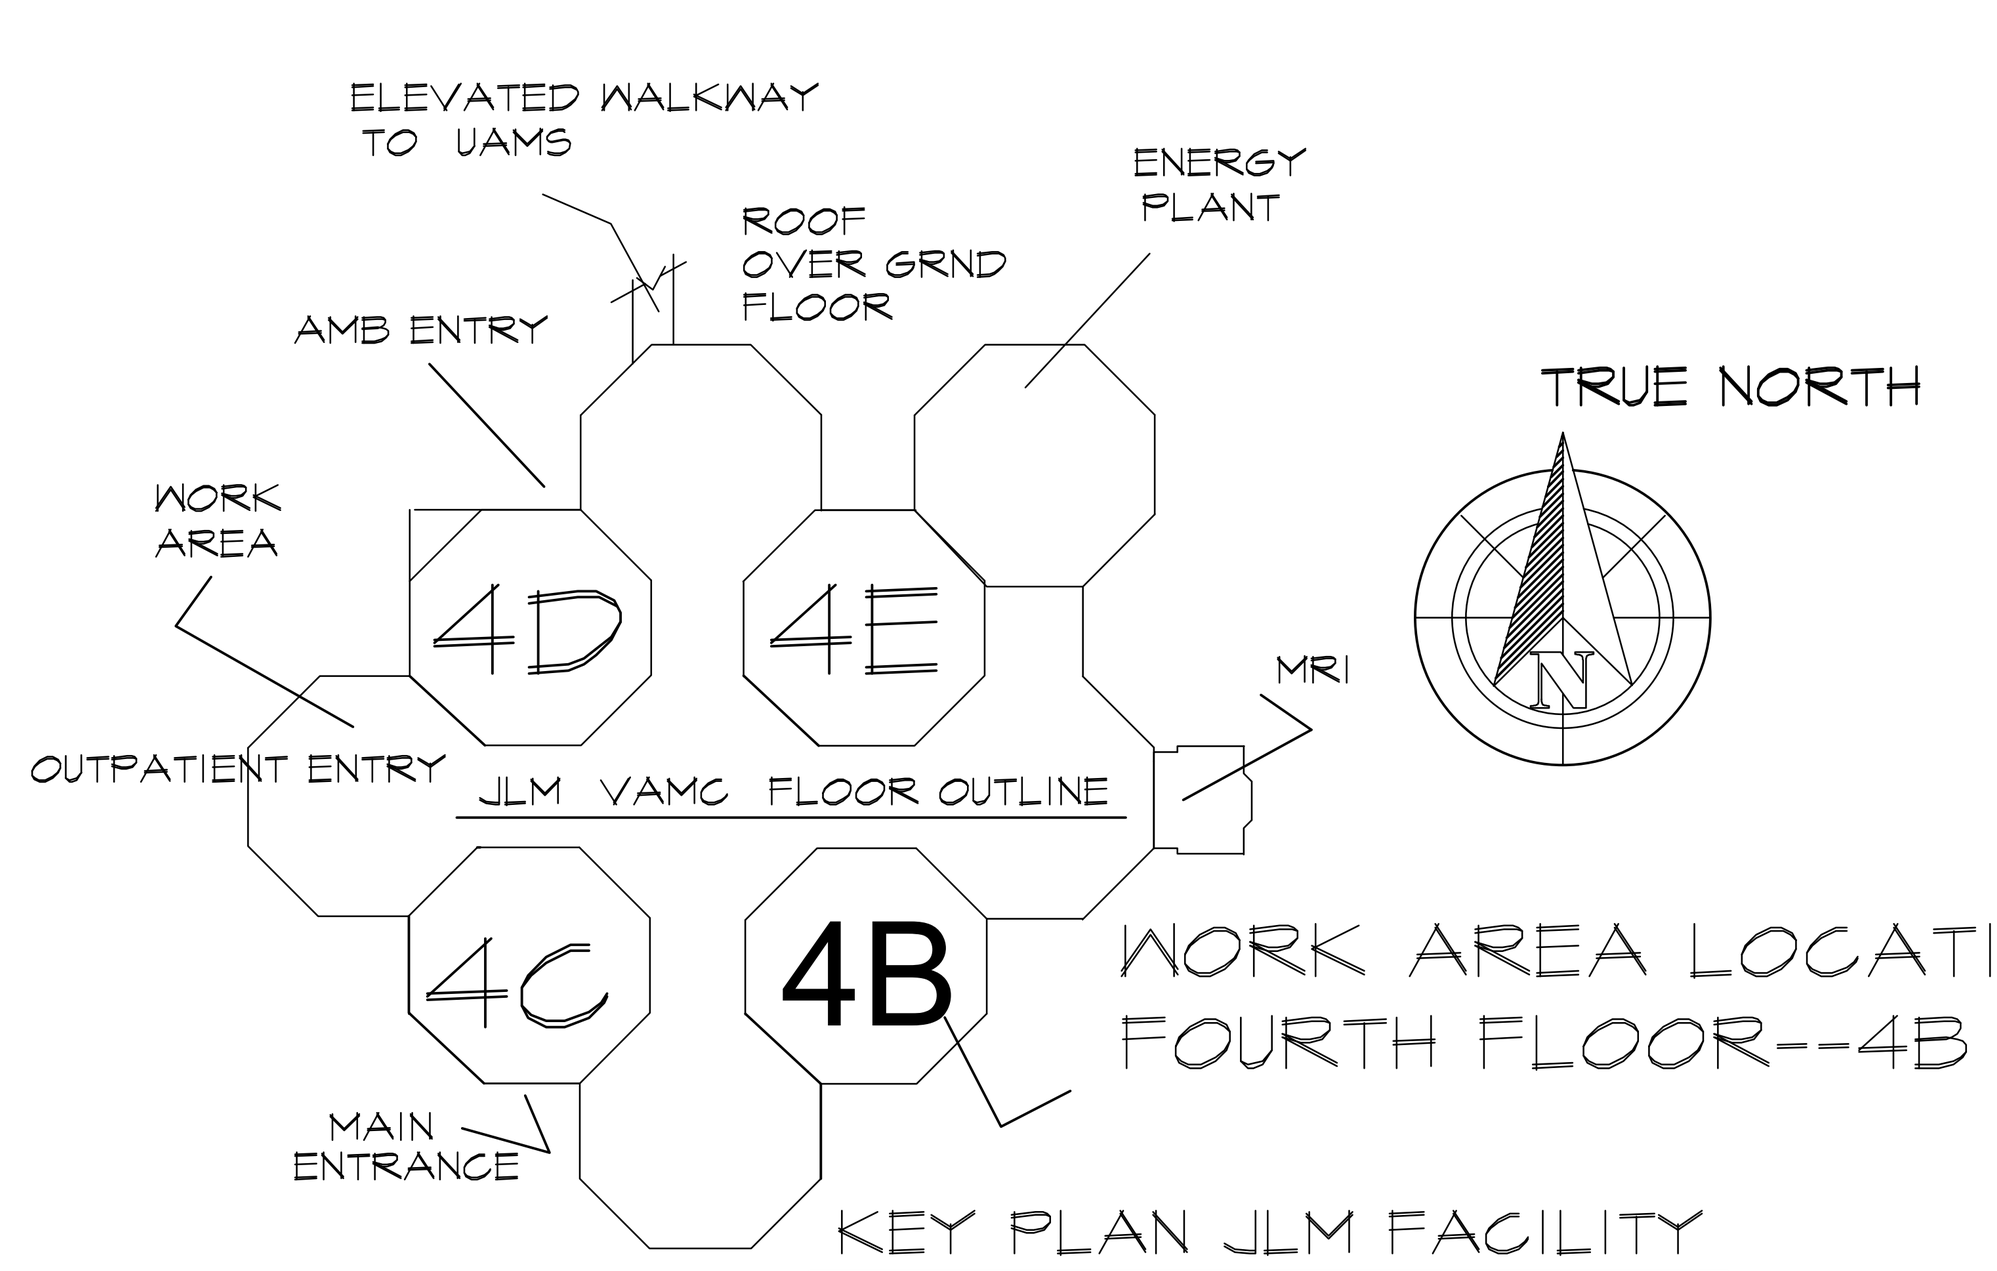

WORK AREA LOCATION
FOURTH FLOOR--4B

KEY PLAN JLM FACILITY

LOCATION PLAN - JLM

PROJECT 598-17-105

REVISIONS	DATE

APPROVED: MEDICAL CENTER DIRECTOR	APPROVED: FACILITY PLANNER	APPROVED: SERVICE CHIEF
APPROVED: ASSOCIATE DIRECTOR	APPROVED: CHIEF ENGINEER	APPROVED: SERVICE CHIEF
APPROVED: ASSISTANT DIRECTOR	APPROVED: SERVICE CHIEF	APPROVED: SERVICE CHIEF

DRAWING TITLE: LR BLDG 1 WORK AREAS PLAN
POD 6E-JLM

PROJECT TITLE: CORRECT LEGIONELLA PROBLEMS

BUILDING NUMBER	CHECKED	DRAWN
1-JLM	KS	RS

LOCATION: V.A.M.C. LR DIVISION

DATE: 7/2017
PROJECT NUMBER: 598-17-105
DRAWING NO.: WA-6E
Dwg 6 of 6

Office of Facilities

DEPARTMENT OF VETERANS AFFAIRS
