
TRAFFIC CONTROL GENERAL NOTES TRAFFIC CONTROL CONSTRUCTION SIGNING AND TRAFFIC CONTROL SHALL CONFORM TO THE MANUAL ON UNIFORM TRAFFIC CONTROL DEVICES (MUTCD) AND AS DIRECTED BY THE CONTRACTING OFFICER'S REPRESENTATIVE (COR) ON CEMETERY PROPERTY. ALL TEMPORARY FIXED LOCATION SIGNS AND APPLICABLE TRAFFIC CONTROL DEVICES SHALL BE INSTALLED PRIOR TO THE START OF WORK IN THE APPLICABLE THE CONSTRUCTION PHASING AND SEQUENCING PLANS WERE DEVELOPED FOR THE CONTRACTOR'S USE. THESE PLANS PROVIDE DETAIL NECESSARY TO MINIMIZE THE DISRUPTION TO USERS. NOT ALL STEPS IN THE PLANS HAVE BEEN IDENTIFIED. IT IS THE INTENT OF THE DESIGNER THAT THE CONTRACTOR WILL SUPPLEMENT THIS SCHEDULE WITH THEIR INTENTIONS TO THE COR AND RECEIVE NECESSARY APPROVAL PRIOR TO THE START OF CONSTRUCTION. THE PHASING AND TRAFFIC CONTROL PLANS INCLUDED WERE PREPARED TO ENABLE THE CONSTRUCTION OF THE IMPROVEMENTS DESCRIBED IN THESE DOCUMENTS TO BE COMPLETED IN A SEQUENTIAL ORDER WITH MINIMAL IMPACT ON THE CEMETERY AND ITS USERS. THE CONTRACTOR SHALL INCORPORATE THE PHASING AND TRAFFIC CONTROL PLANS INTO HIS SEQUENCE OF OPERATIONS. THE CONTRACTOR WILL NOT BE PERMITTED TO WORK CONCURRENTLY ON MULTIPLE PHASES. ANY MODIFICATIONS TO THE PHASING, SEQUENCING OR TRAFFIC CONTROL DESCRIBED IN THESE DOCUMENTS SHALL BE APPROVED, IN WRITING, BY THE COR. REQUESTS FOR VARIATIONS TO THE PHASING, SEQUENCING, OR TRAFFIC CONTROL SHALL BE SUBMITTED TO THE COR FOR REVIEW A MINIMUM OF TWO (2) WEEKS PRIOR TO IMPLEMENTATION. THE REQUEST SHALL INCLUDE A DETAILED DESCRIPTION OF THE CHANGE REQUESTED. ALTERNATE PHASING, SEQUENCE OF OPERATIONS OR TRAFFIC CONTROL WILL ONLY BE ALLOWED WHEN THE PROPOSED CHANGES MEET WITH THE OWNER'S INTENT FOR TRAFFIC CONTROL AND MAINTENANCE OF SERVICE. PHASE WORK LIMITS ARE GENERALLY AS SHOWN ON THIS PLAN AND AS DESCRIBED HEREIN. DETAILS OF THE WORK ITEMS ARE SHOWN THROUGHOUT THESE PLANS. ALL UNDERGROUND AND ROADWAY WORK INCLUDING FINAL RESTORATION SHALL BE COMPLETE PRIOR TO THE CONTRACTOR MOVING TO THE NEXT PHASE THE CONTRACTOR SHALL PROVIDE TEMPORARY GRAVEL SURFACING FOR TEMPORARY TRANSITIONS BETWEEN PHASES. PEDESTRIAN PROTECTION PROTECTION OF PEDESTRIAN TRAFFIC FROM OPEN EXCAVATIONS AND OTHER HAZARDS IN AND AROUND THE CONSTRUCTION SITE SHALL BE IN COMPLIANCE WITH OSHA, THE AMERICANS WITH DISABILITIES ACT AND AS DIRECTED BY THE COR. **CHANNELIZING DEVICES**

VA FORM 08-623

NOTES:

- 1. CONTRACTOR SHALL PROVIDE ACCESS AT ALL TIMES TO VISITORS. AT A MINIMUM, VEHICULAR TURN-AROUND AND/OR ONE-WAY CONTINUOUS VEHICULAR TRAFFIC ROUTE(S) SHALL BE PROVIDED. CONSTRUCTION MAY BE PHASED AS SHOWN HEREON OR AS APPROVED BY OWNER.
- 2. TEMPORARY SIGNAGE WILL BE REQUIRED AS SHOWN HEREON OR AS APPROVED BY COR. TEMPORARY TRAFFIC PLAN PREPARED BY CONTRACTOR SHALL BE REQUIRED FOR ALTERNATE PLANS.
- 3. THIS CEMETERY IS CLOSED TO NEW INTERMENTS. HOWEVER, LIMITED BURIALS FOR FAMILY MEMBERS ARE AVAILABLE.
- 4. COORDINATE ALL WORK WITH CEMETERY SCHEDULES AND ACTIVITIES. CEREMONIES ARE EXPECTED (BUT NOT LIMITED) TO OCCUR ON OR AROUND MEMORIAL DAY AND VETERANS DAY. REFER TO SPECIFICATION 01 00 02, PARAGRAPH 1.6.0.
- 5. CONTRACTOR EQUIPMENT, MATERIALS, AND WORKMAN ARE NOT PERMITTED ONTO THE CEMETERY GROUNDS OR GRAVESITE AREAS. ALL CONTRACTOR ITEMS MUST REMAIN ON PAVEMENT OR IN PRE-APPROVED STORAGE AREAS, NOT WITHIN BURIAL AREAS OR ON GRAVESITES. NO SMOKE BREAKS OR LUNCH BREAKS IN GRAVESITE AREAS.




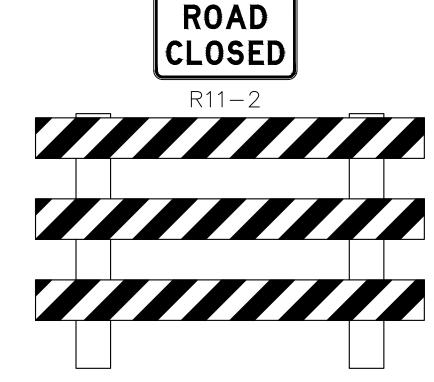








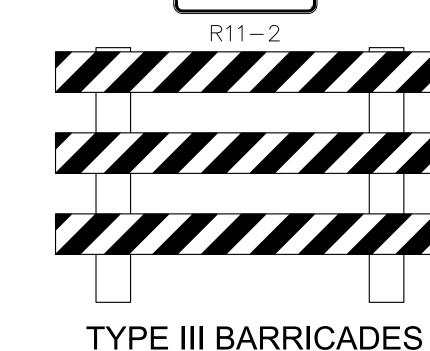


THE FOLLOWING GENERAL RULES ON DELINEATION APPLY:

• ORANGE SAFETY CONES OR CONCRETE BARRIERS SHALL BE USED TO DELINEATE TAPERS AND LANE SHIFTS AND TO SEPARATE TRAFFIC FROM WORK AREAS.

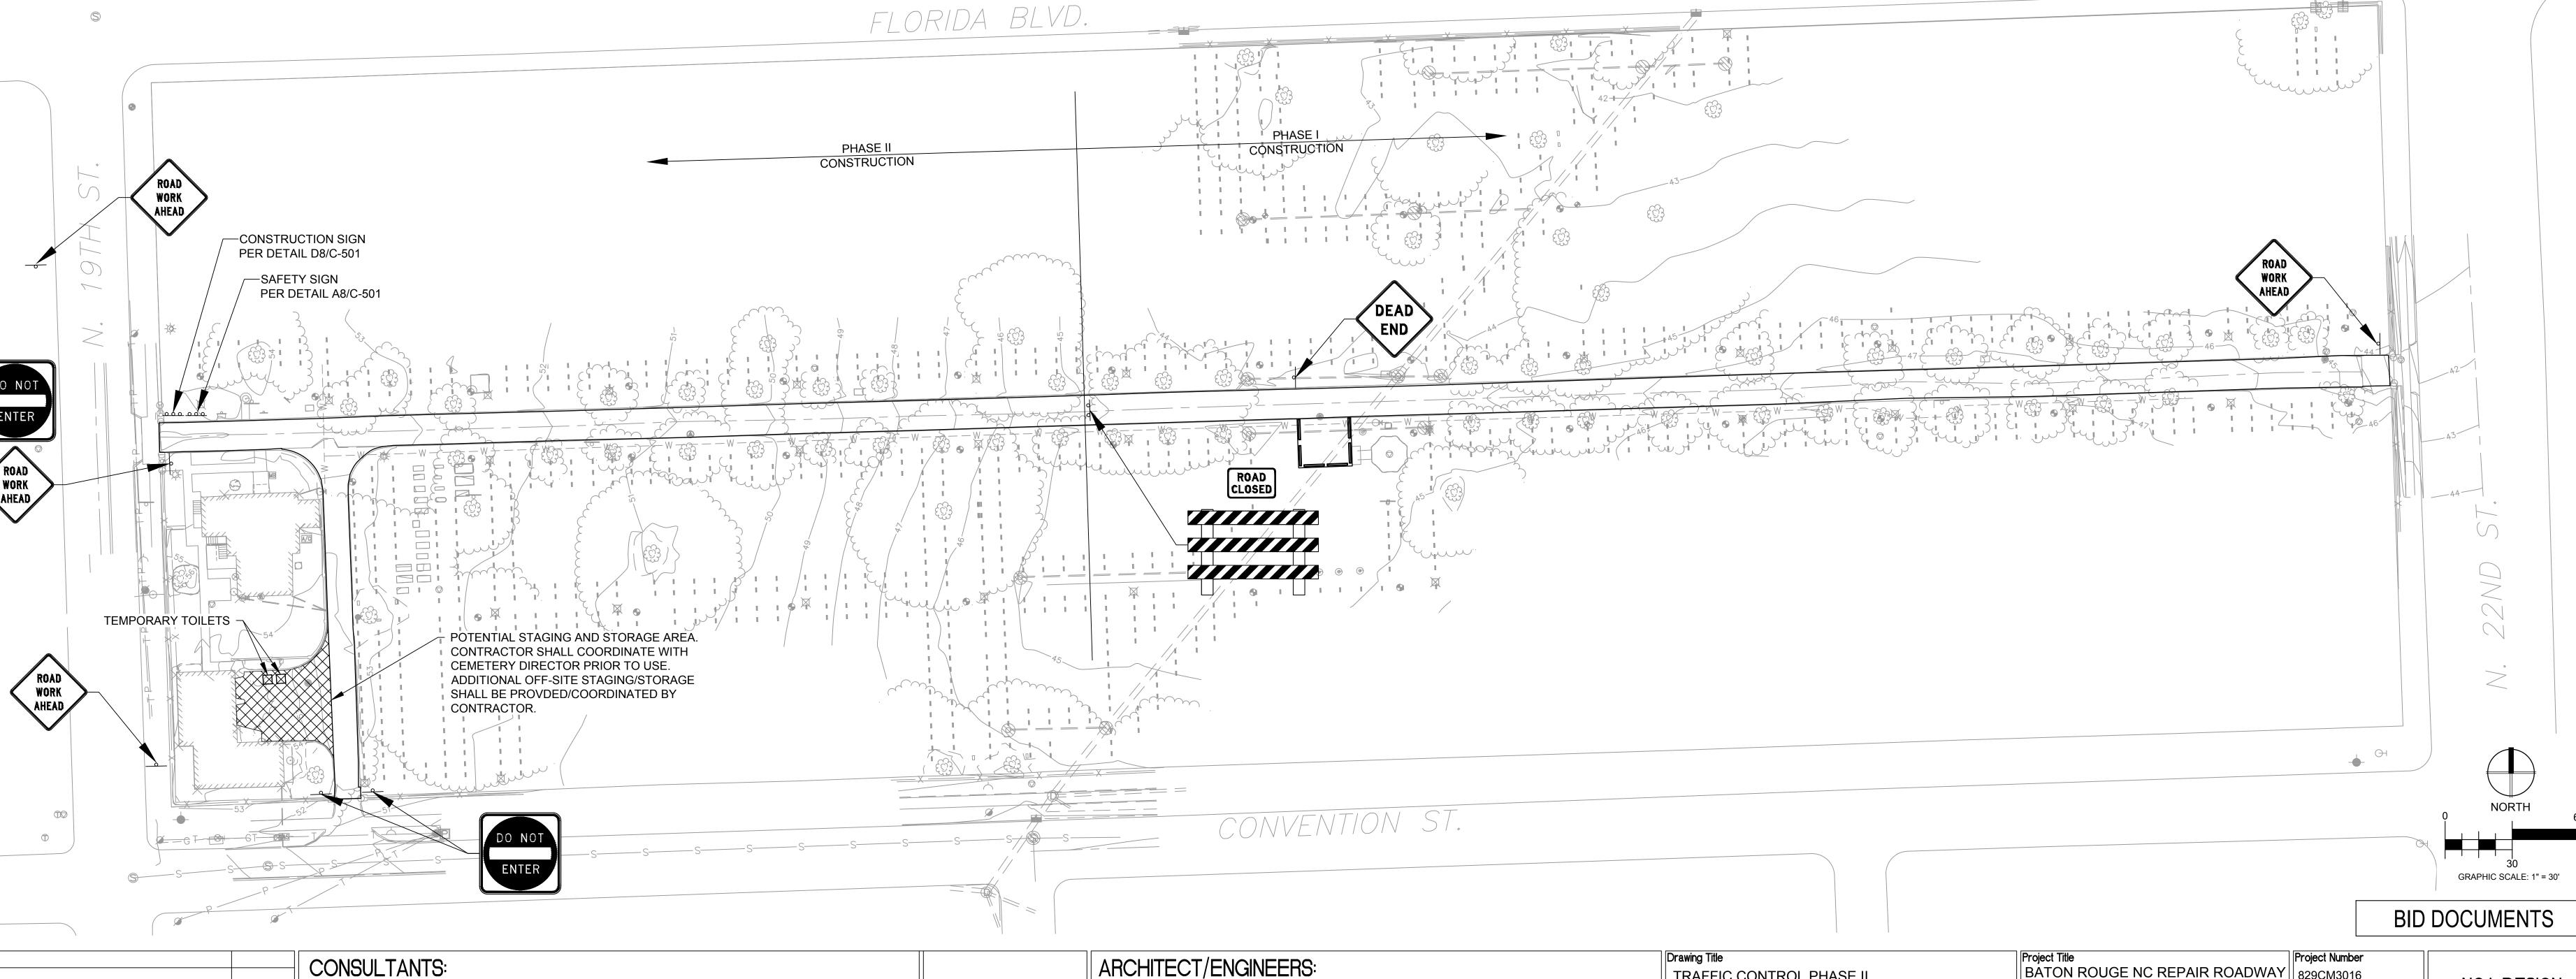

CONSULTANTS: BATON ROUGE LAND SURVEYING CH2MHILL® llerracon Consulting Engineers and Scientists A Division of Forte & Tablada
9107 INTERLINE AVE. BATON ROUGE, LA 70809 PH: (225) 752-0336 6600 Peachtree Dunwoody Road 2822 O'Neal Lane Bldg B Baton Rouge, LA 70816 p (225) 344-6052 f (225) 344-6346 400 Embassy Row, Suite 600 Office: (678) 401-7955





Preliminary Not For Construction

6

BATON ROUGE NC REPAIR ROADWAY 829CM3016 TRAFFIC CONTROL PHASE II Building Number Approved: Project Director Location BATON ROUGE NATIONAL CEMETERY BATON ROUGE, LA C-103 CZ Dwg. 7 of 9

NCA DESIGN AND CONSTRUCTION SERVICE Department of Veterans Affairs

3
